PROJECTFLOW

User Manual

Raman C Nair

Table of Contents

1. Setup Wizard 4
   - Database 4
   - Authentication 5
   - Super Admin User Creation 6
   - AI Configuration 7
   - Finish 8
2. Signup and Login flow 9
   - Home 9
   - Signup 9
   - Login 10
3. Portfolio Flow 11
   - My Projects 11
   - Projects 12
     - Project Home 12
     - Portfolio Dashboard 13
   - Quality 14
     - Estimations 14
     - Defects 15
   - Billing 16
   - Users 17
     - User List 17
     - Utilization 18
   - Holidays 19
     - Holiday Calendar 19
     - Leave Settings 19
     - Leave Tracker 20
4. Initial Estimation Flow 21
   - Project Home 21
   - Initial Estimation 21
5. Project Flow 25
   - Project Details 25

Project Status 25
PM Dashboard 26
Specifications 27
Resources 28
Project Resources 28
Worklog 29
Resource Workload 29
Releases 30
Development 31
Development Dashboard 31
Product Backlog 31
Sub-Tasks 34
Grooming 35
Kanban Board 36
Testing 37
Testing Dashboard 37
Test Backlog 38
Test Plan 38
Defects 39
Defect Tracker 40
Governance 41
RAID Dashboard 41
Risks 41
Assumptions 42
Issues 42
Dependencies 43
Holidays 44
Holiday Calendar 44
Leave Calendar 44
PMO 46
Project Documents 46
FB Billing (Fixed Bid Billing) 47

FB Payment Milestones 48
Business Continuity 49
TnM Billing (Time & Matierial)..... 50
TnM Payment Milestones 51
6. Admin Flow..... 52
Portfolio Settings 52
Access Settings 52
Database..... 53
Authentication 54
AI Configuration 54
Archive 55
Trash 56

1. Setup Wizard


When you are opening the ProjectFlow app for the first time, you will be presented with a setup wizard to enter essential configuration details and create the Super-Admin user.

Database

Project Name – This is the identifier name for this DB


Database Provider – Currently supports Firebase (cloud) and Supabase (cloud/docker)

Firebase Project ID, Firebase API Key – These details you can copy from the firebase console

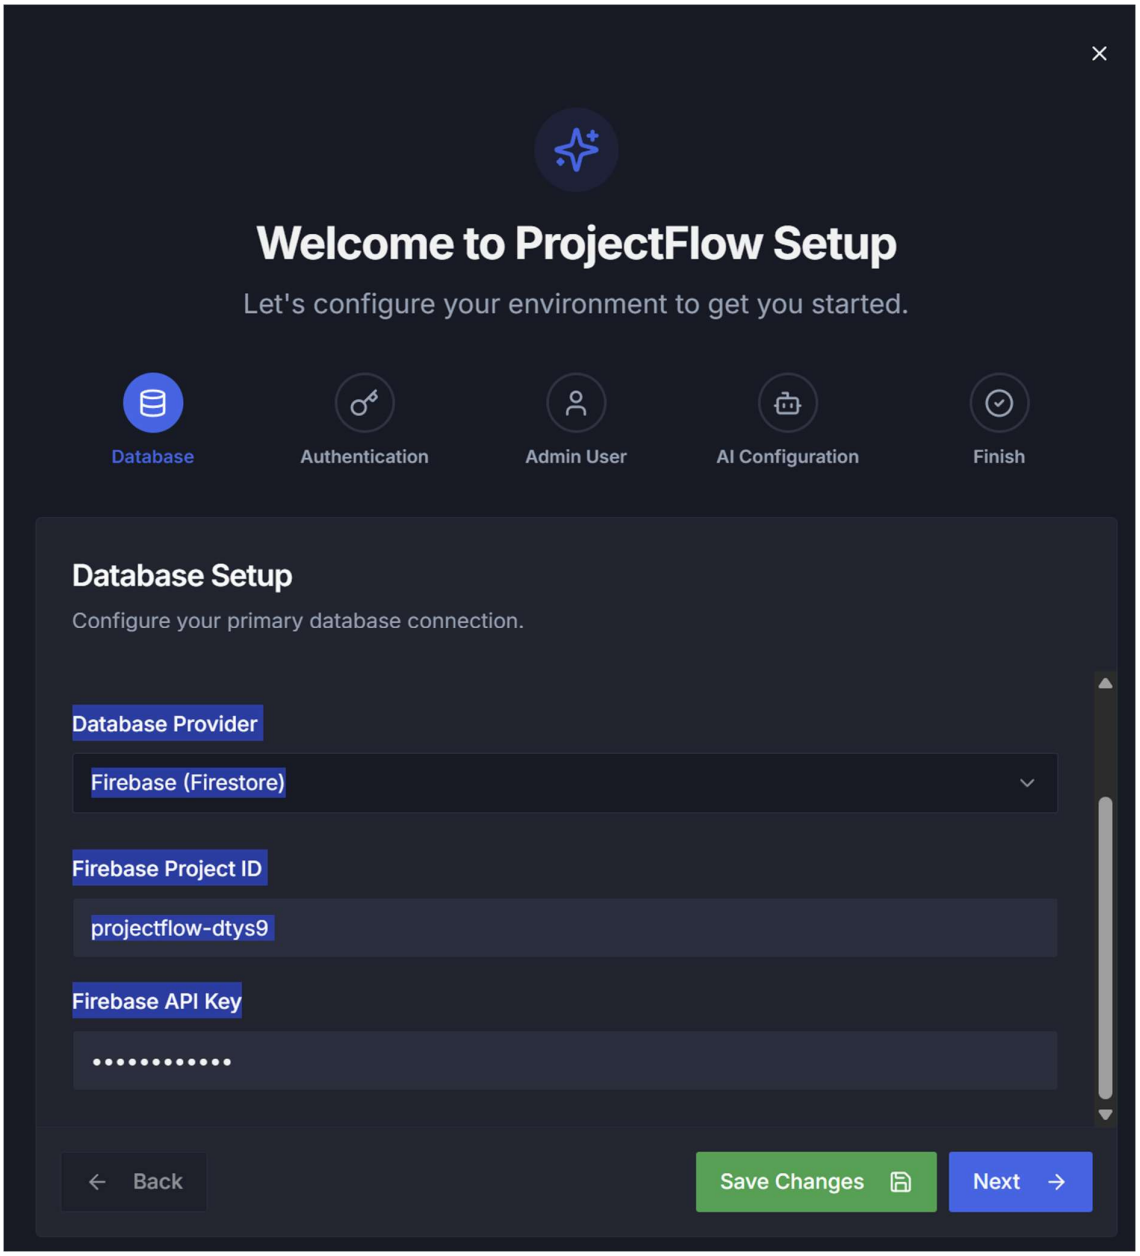


Authentication

If your DB is firebase, the app will use Firebase Auth. If your DB is Supabase, it will use Supabase Auth.

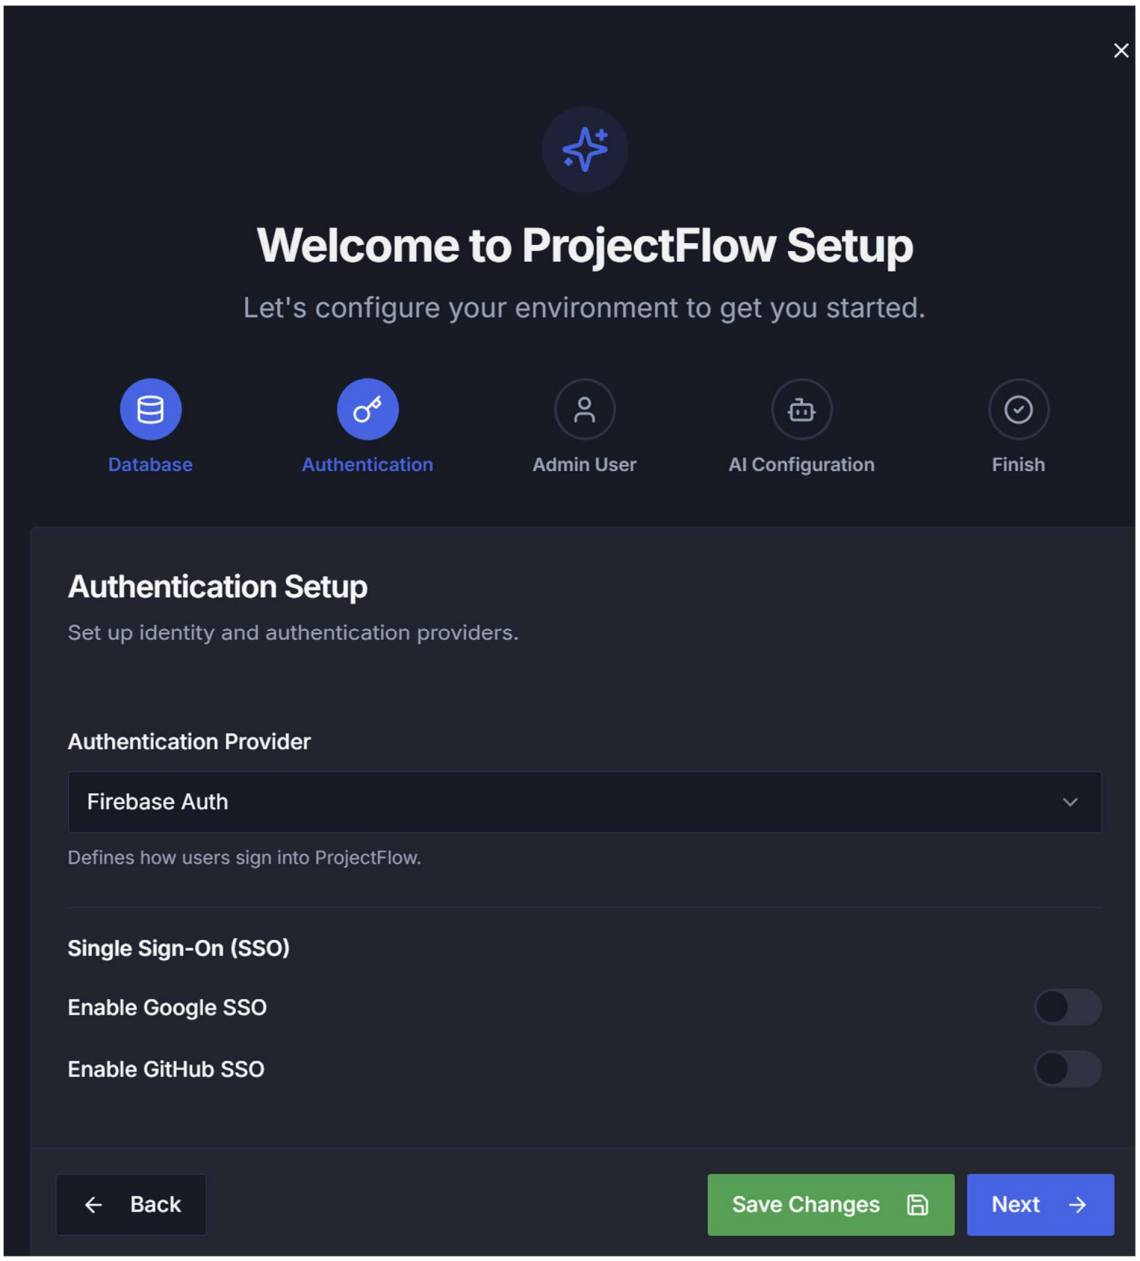

Super Admin User Creation

Now that the DB connectivity and Auth is established, the first user that the app creates is the SuperAdmin.

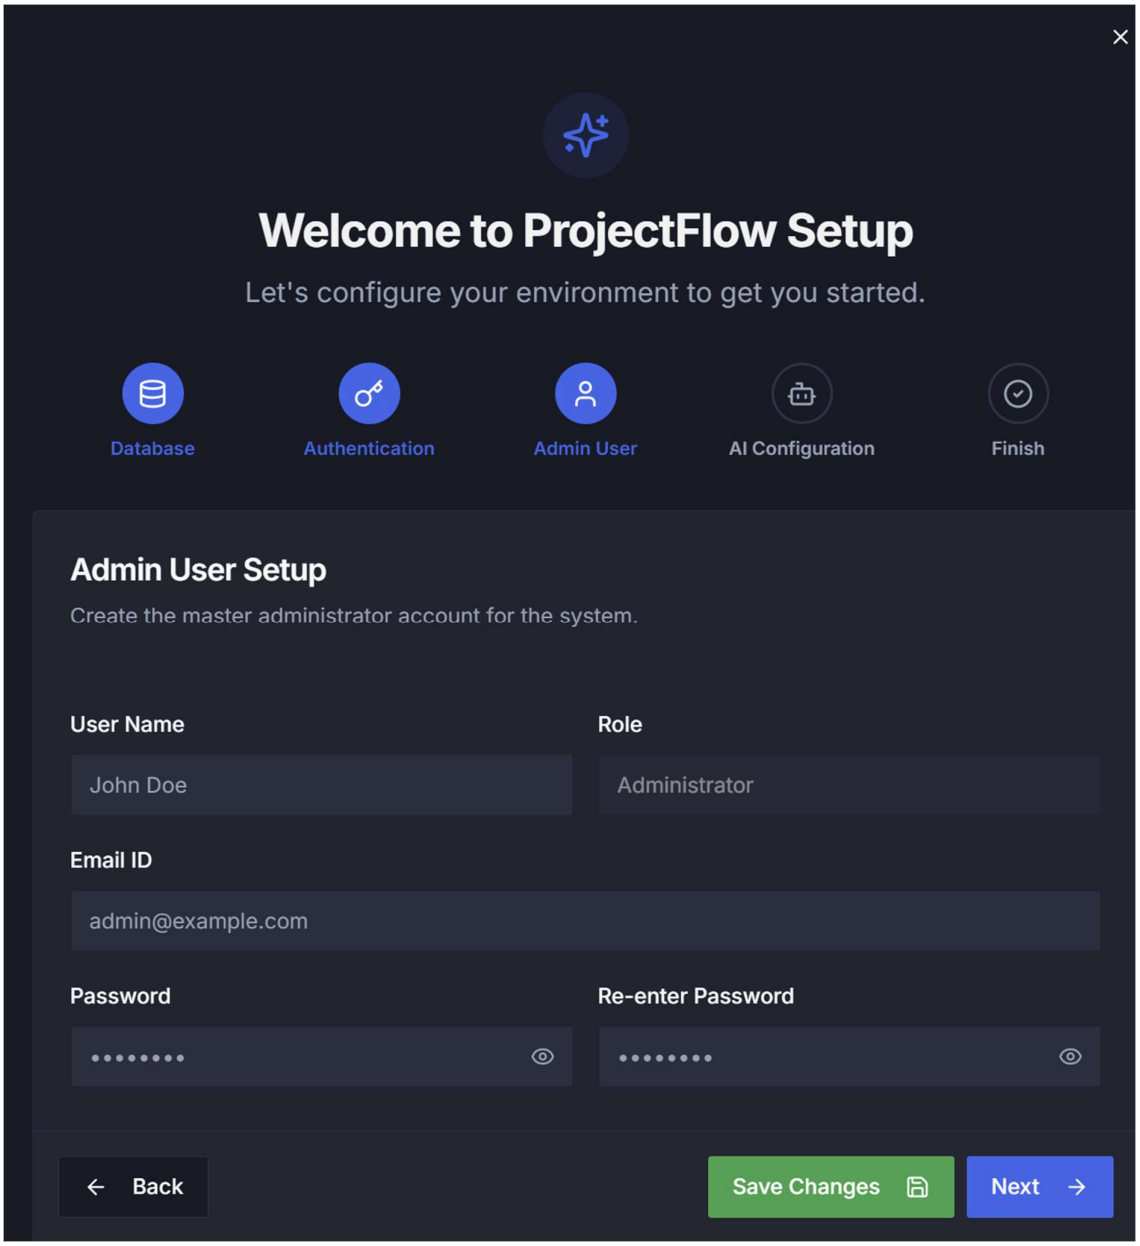

AI Configuration


The app will run without AI also. Only the AI support functionalities will not work.

Project Name – This is the identifier for this particular configuration


AI Provider – Currently supports Gemini, Claude, ChaptGPT, Ollama and LM Studio

API Key – Get from the provider sites

Default Model Override (Optional)

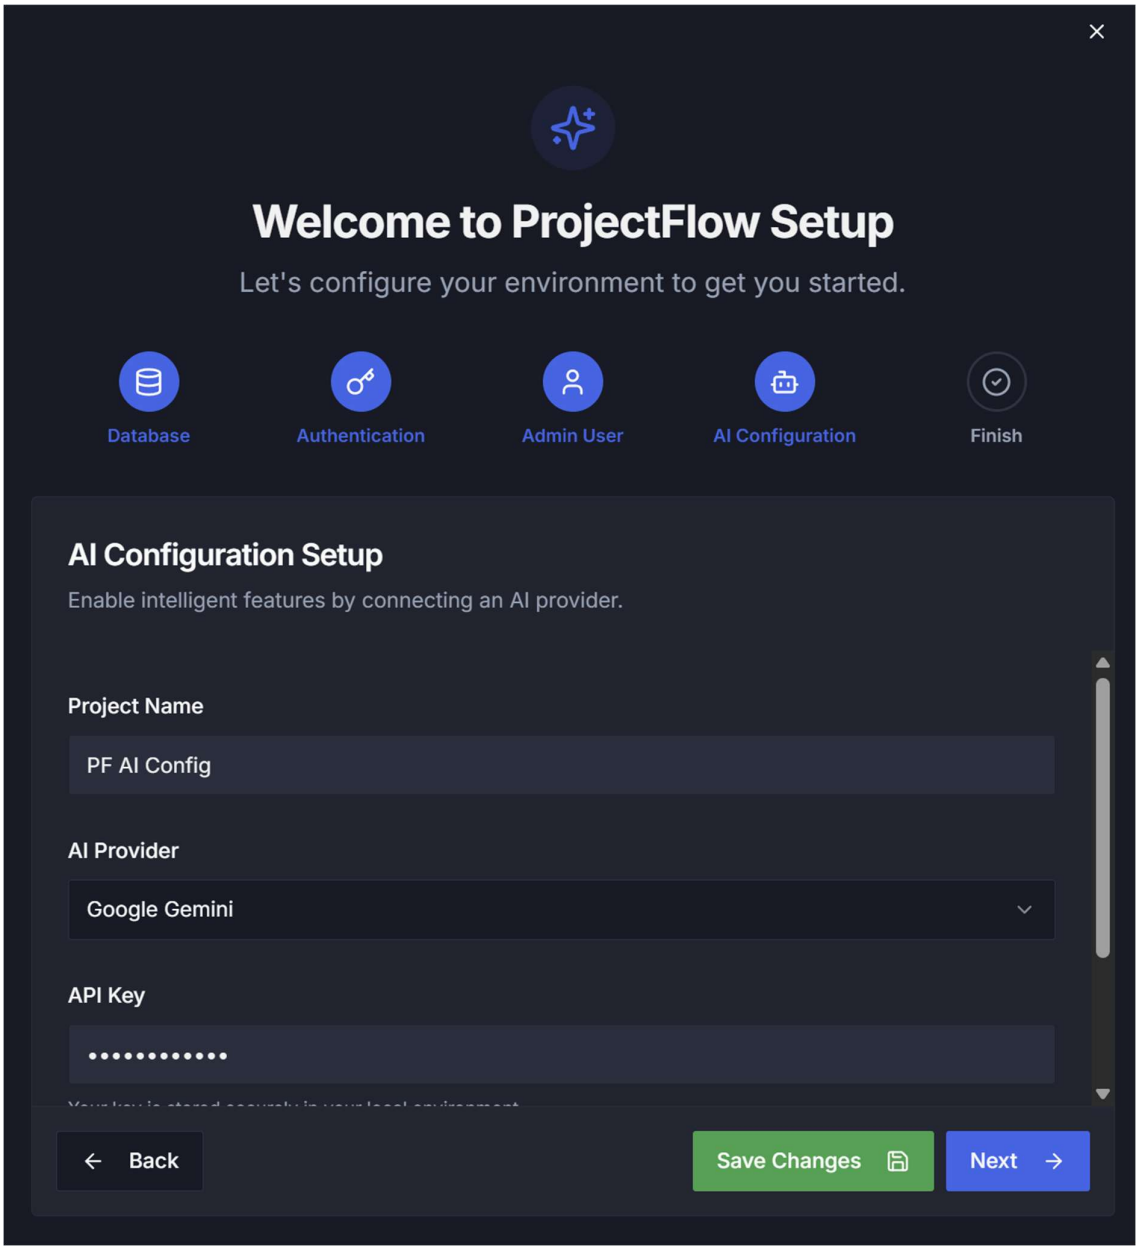


Finish

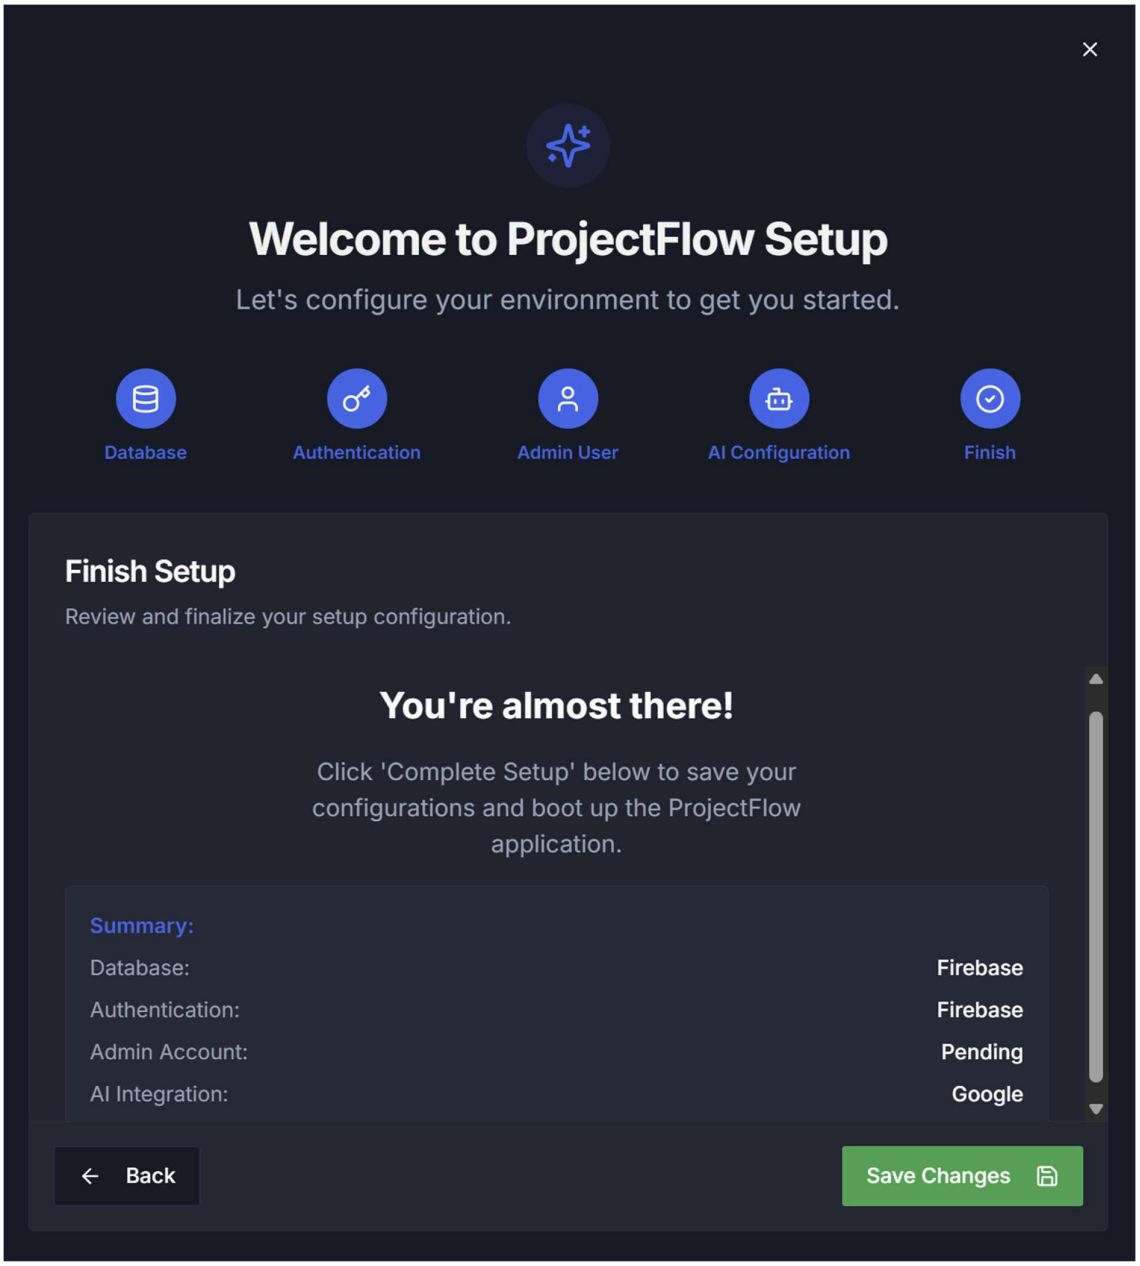
Welcome to ProjectFlow Setup
Let's configure your environment to get you started.
Database
Authentication
Admin User
AI Configuration
Finish
Finish Setup
Review and finalize your setup configuration.
You're almost there!
Click 'Complete Setup' below to save your configurations and boot up the ProjectFlow application.
Summary:
Database: Firebase
Authentication: Firebase
Admin Account: Pending
AI Integration: Google
Back
Save Changes

2. Signup and Login flow


Home

Landing page.

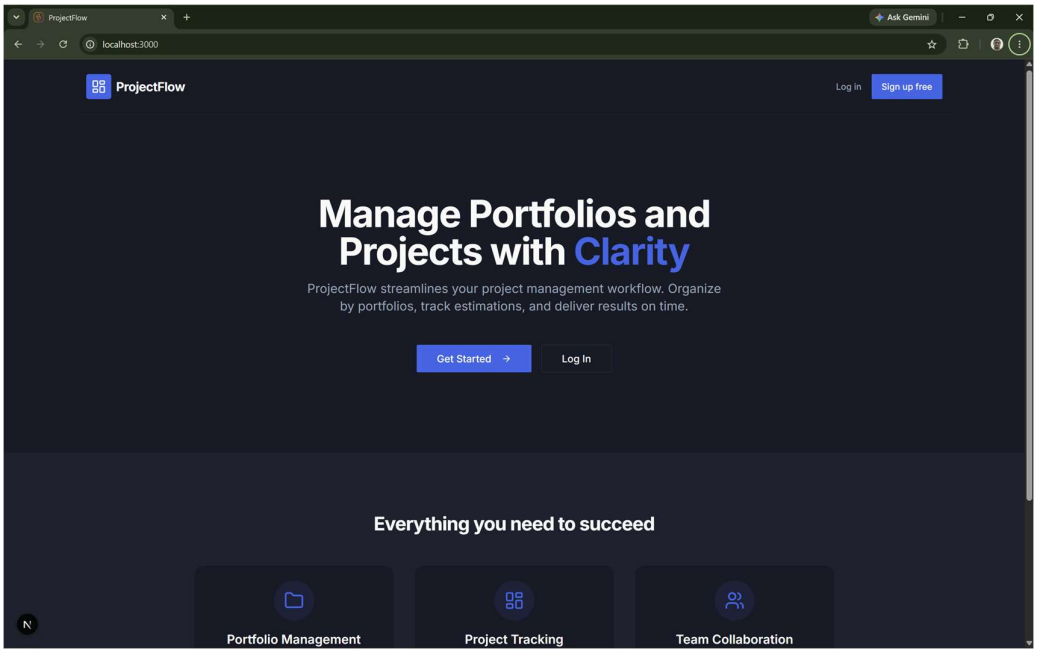


Signup

For creating a new user, you need to sign up. Once signed up, the user will be able to see only the My Projects page. Once the user has been enabled by the Admin, they can see the remaining pages.

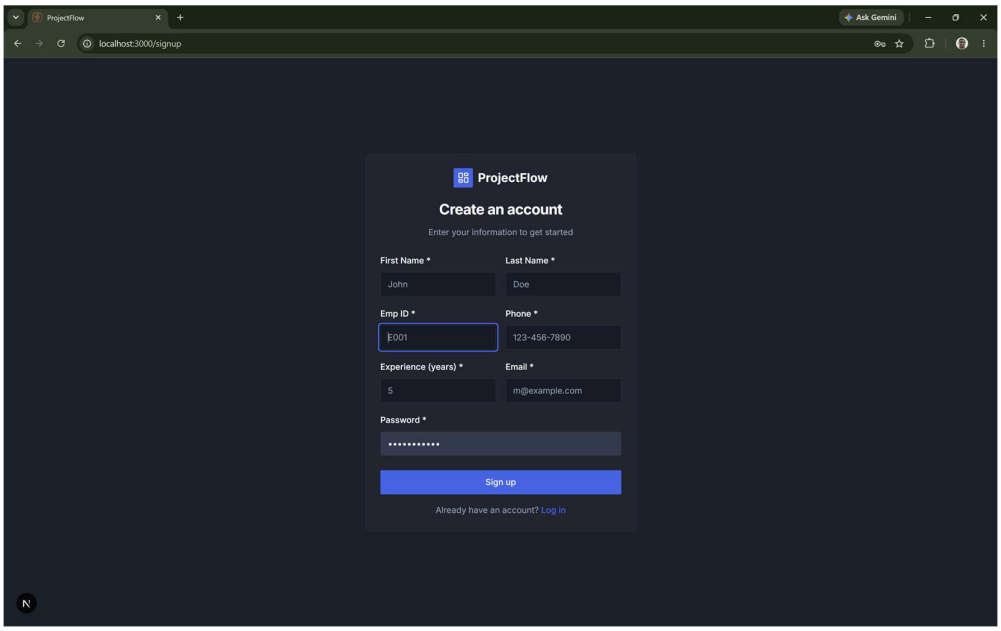

Login


If the user is already created by Admin, then they will have to login using their registered email and the default password – “P@ssw0rd”. They will then be redirected to update their password.

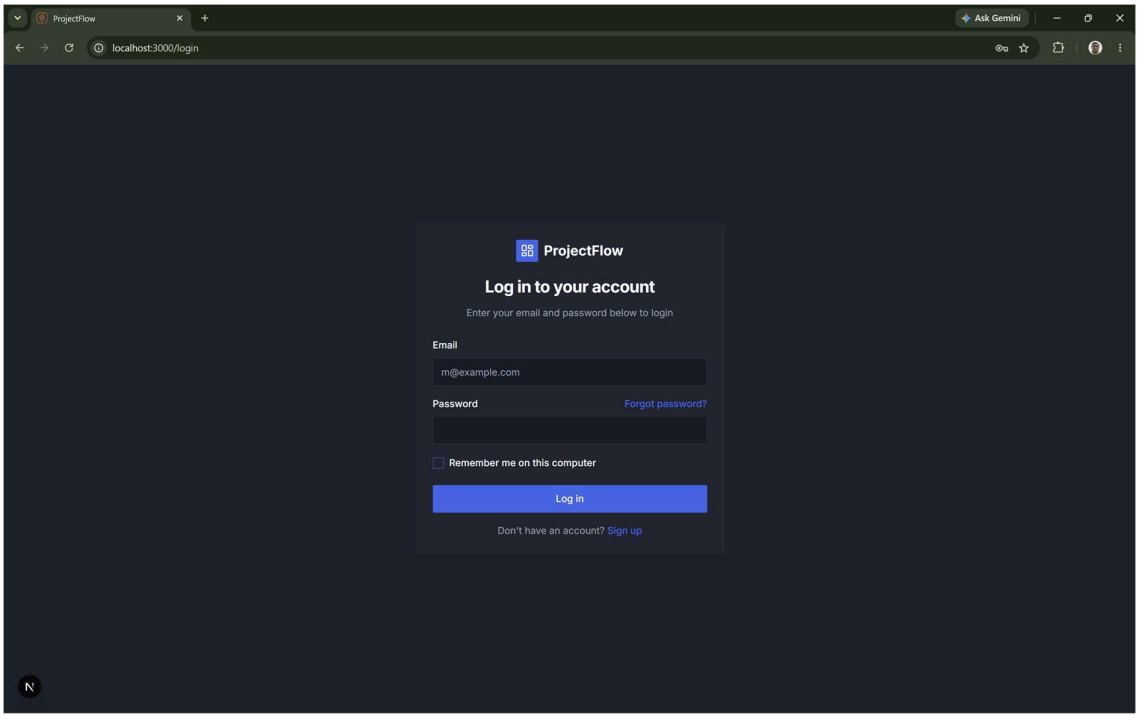

3. Portfolio Flow

My Projects


This page will show the list of projects the user is assigned to. For PMs, they will also be shown the Initial Estimations they are assigned to.

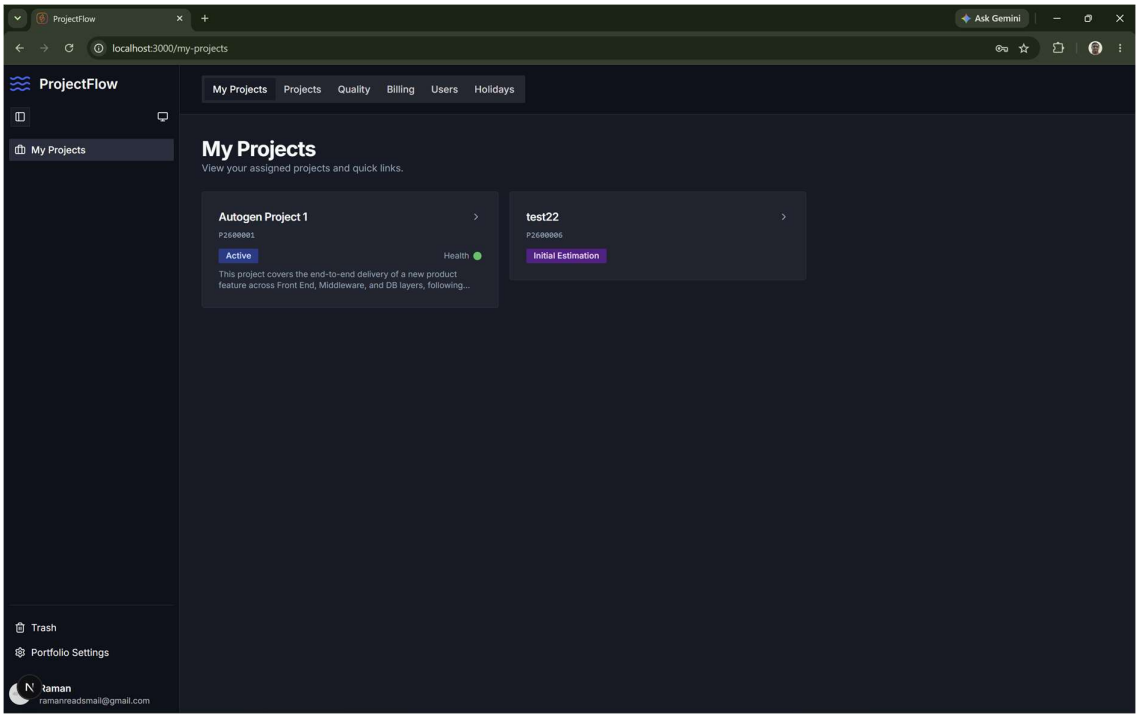


Projects

Project Home

This is the total list of all projects and initial estimations which are not closed.

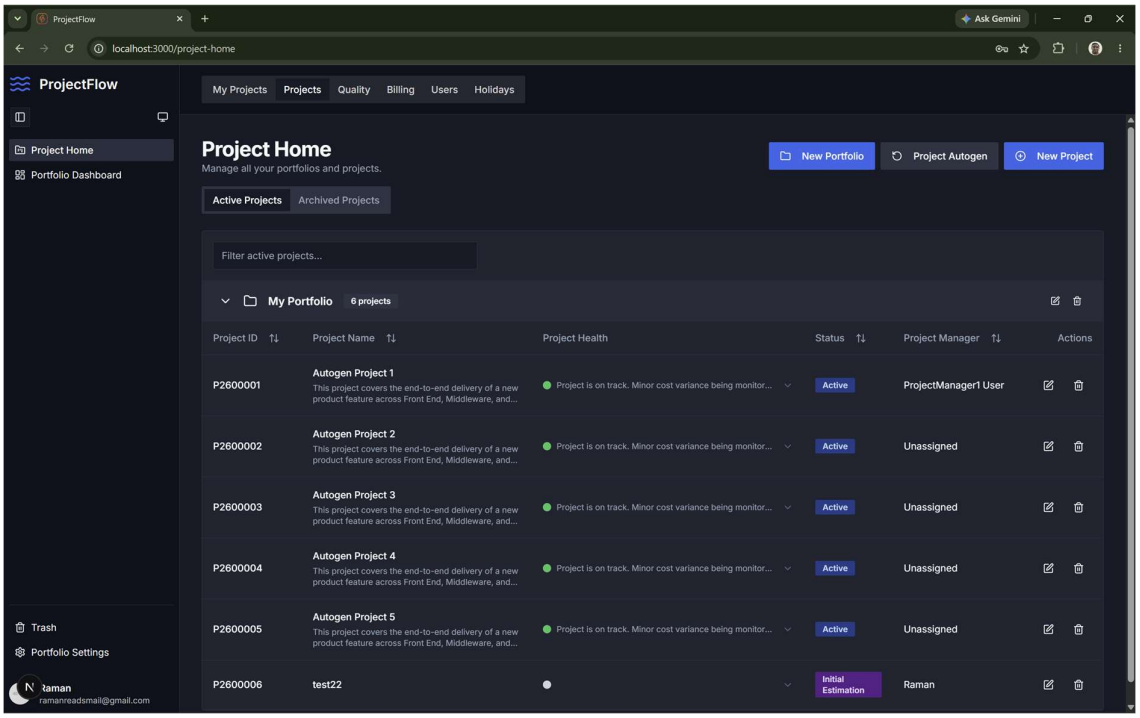


Before creating a project, we should create a Portfolio. Because all projects have to part of a portfolio. If you want to leave Unassigned, create an Unassigned Portfolio and assign to it.

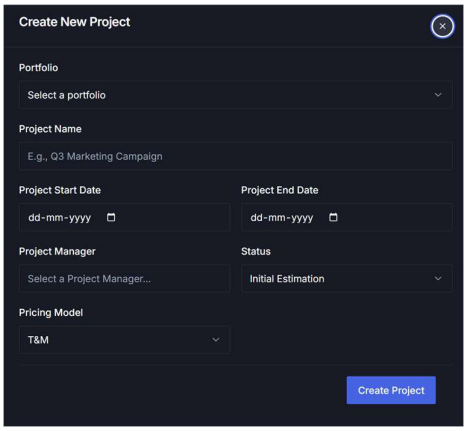

Portfolio Dashboard


This is the status of the active projects which needs attention. Only those projects will have status red or yellow will be shown. This page is targeted for upper management.

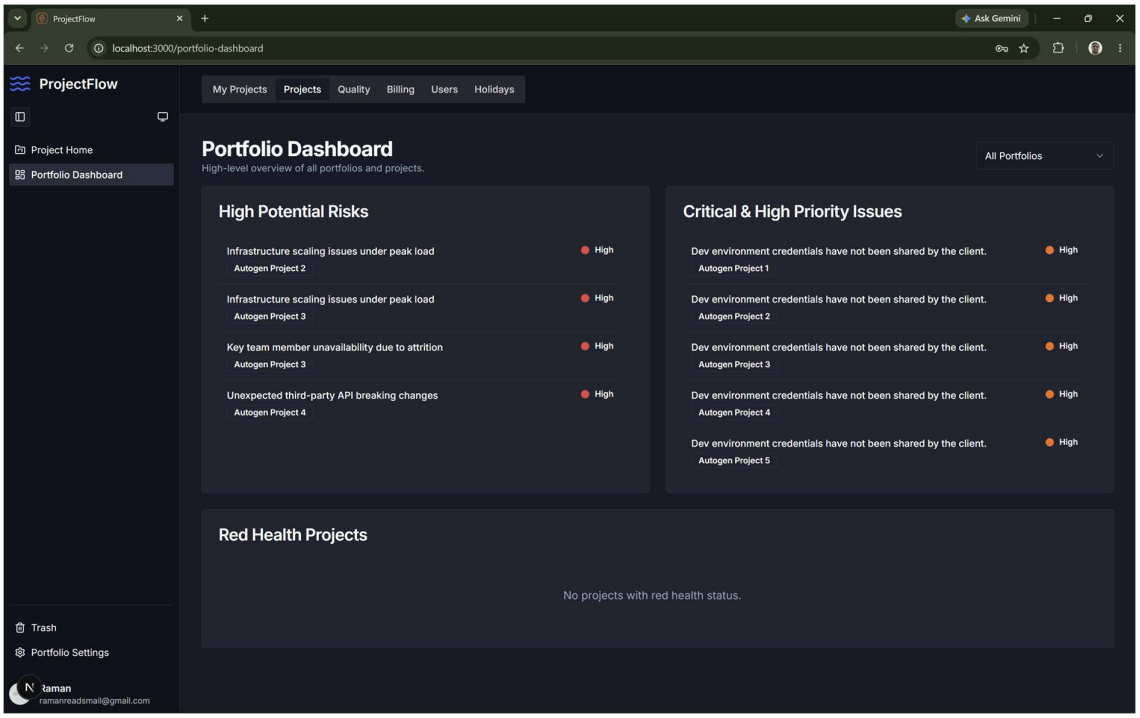

Quality


Estimations

This pages shows the estimations given for a project when it was in Initial Estimation stage (The estimate given when requirements were at high level), Planned Estimation (The estimation given after all the stories are written and sub-tasks which are the requirements for each impacted system for that story are estimated.) and the actual effort taken to complete (Taken from worklog). This will give the upper management an idea if their estimations variance is too much and take measures to bring it under control. This is critical since the billing is based on estimation.

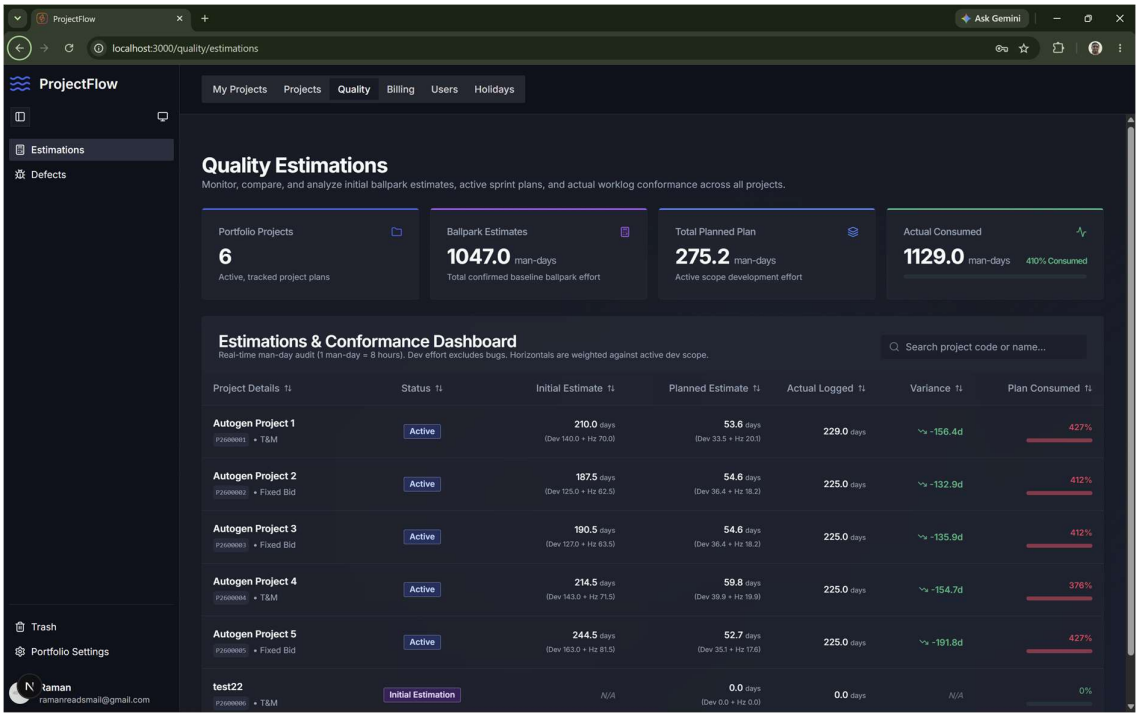


Defects

This will show the number of defects occurring at each stage of testing and give an idea as to whether the QA teams are catching the bugs early enough in the process.

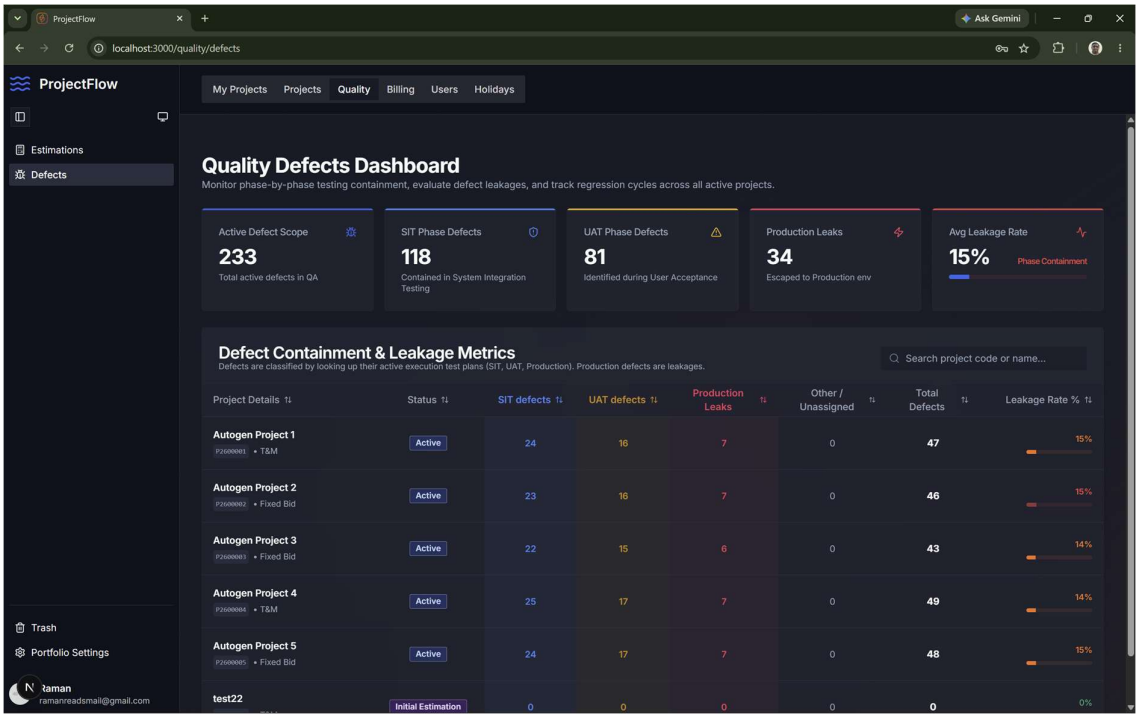

Billing


This page lists the revenue from a project (Total revenue if Fixed Bid, Monthly revenue accumulated till the previous month for Time & Material projects). It also lists the resource cost and the fixed costs (server set up costs, GIT, licenses etc. which are mentioned inside the project), Profit and actual realized (Since there might be a delay in actual payment from the client after raising the invoice.)

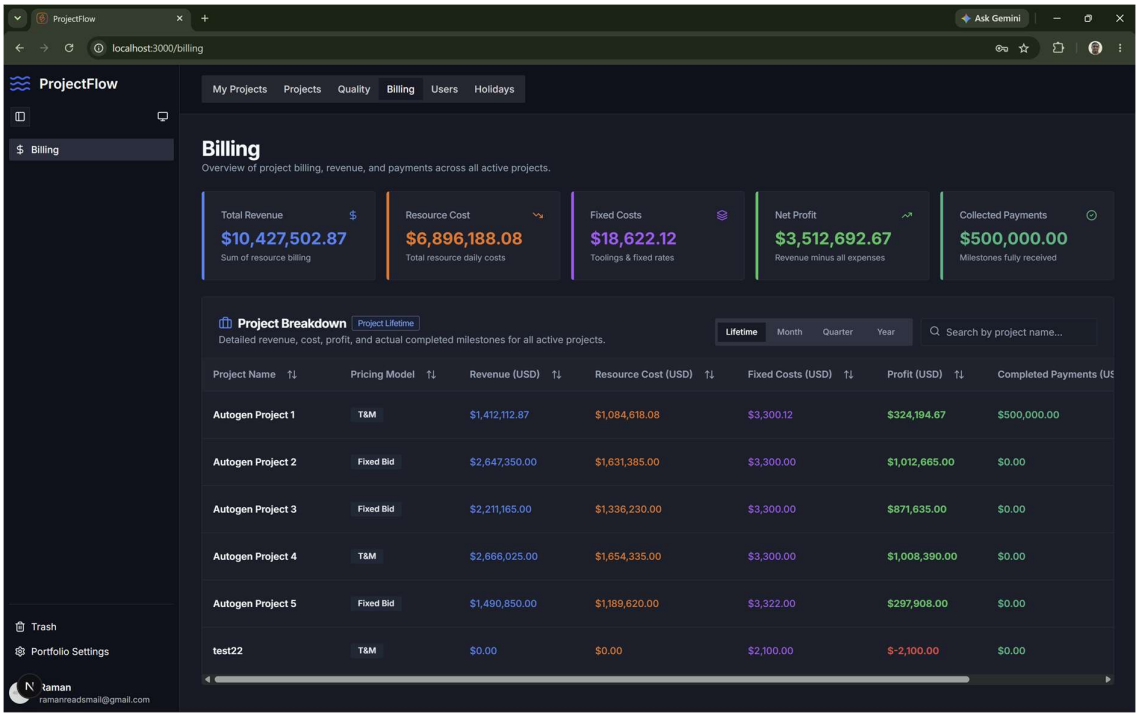


Users

User List


List of users registered with the app. The new users who have to be enabled will be shown as a notification to upper management to approve. The Admin can directly add a new user here without requiring them to sign up.

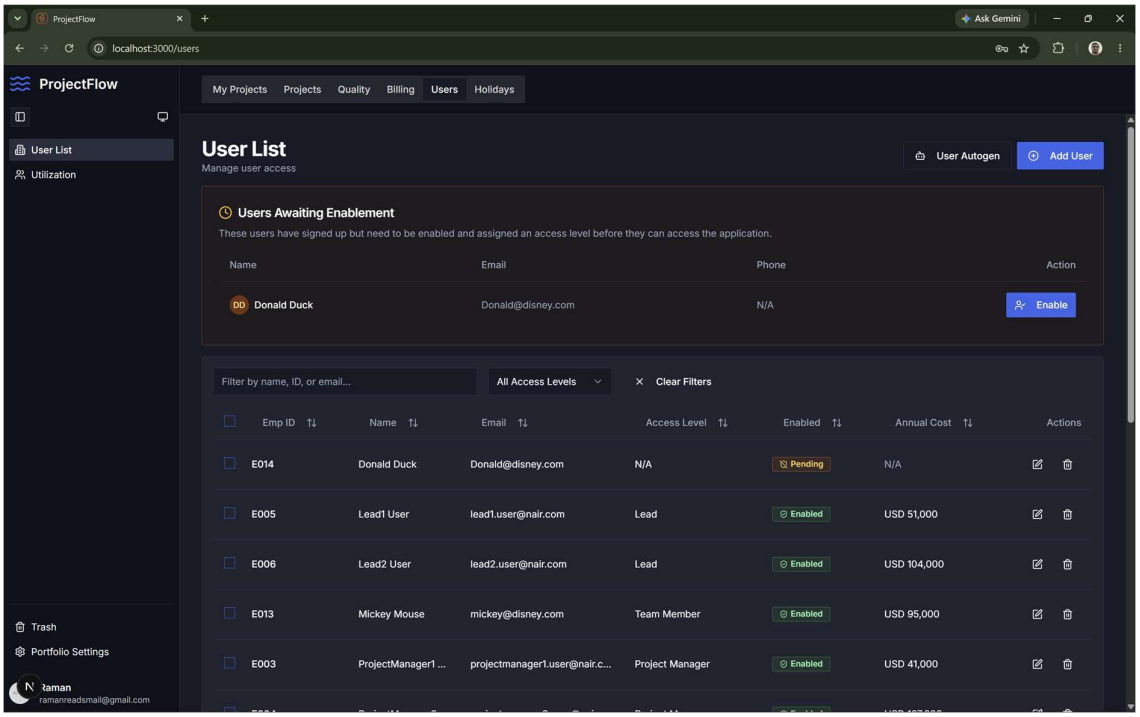

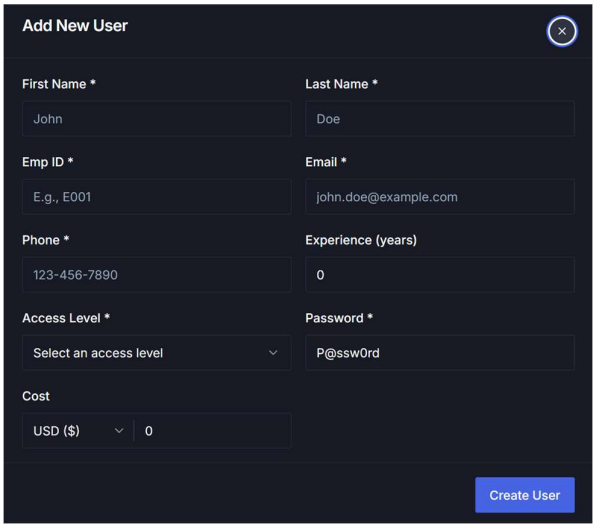

Utilization


Search by the user name to see the projects they are working on and till how long they will be working on that project and see when they will be available.

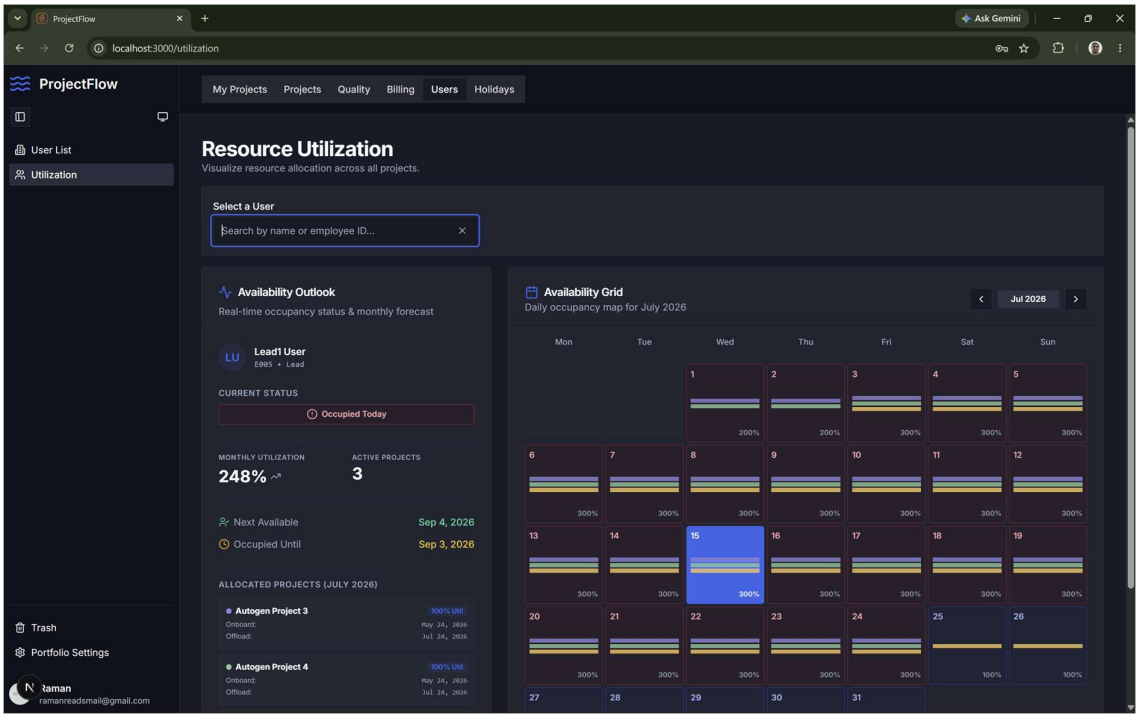

Holidays


Holiday Calendar

Here we can declare the global weekend (time off) days and the yearly holidays. Projects will be taking from here the default values

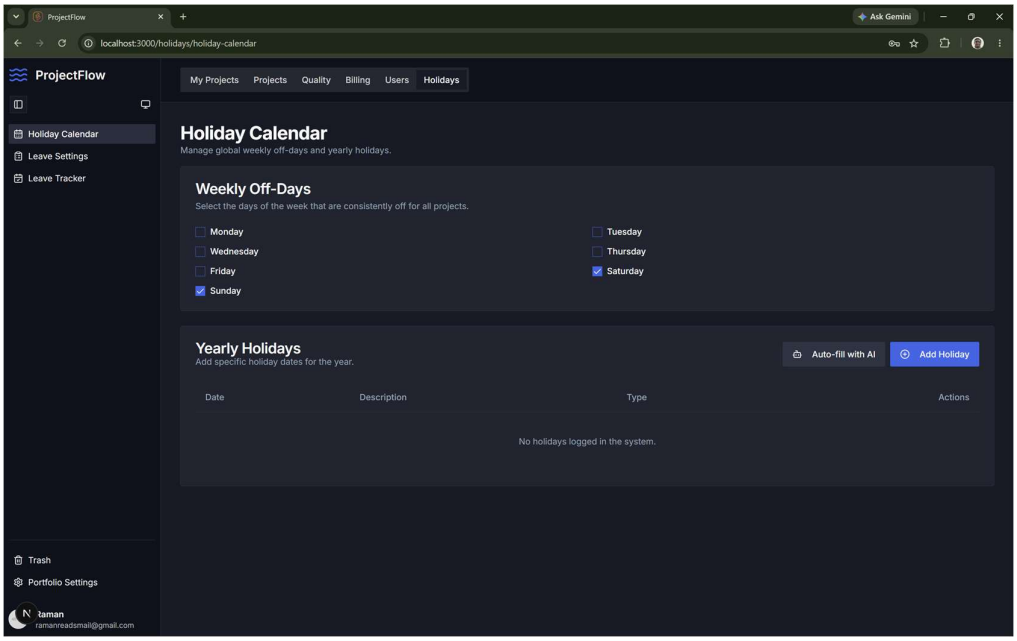


Leave Settings

Global setting for how many leaves is allowed for each person. You can also allow carryover leaves as per your company policy and the number of leaves you are allowed to carry over.

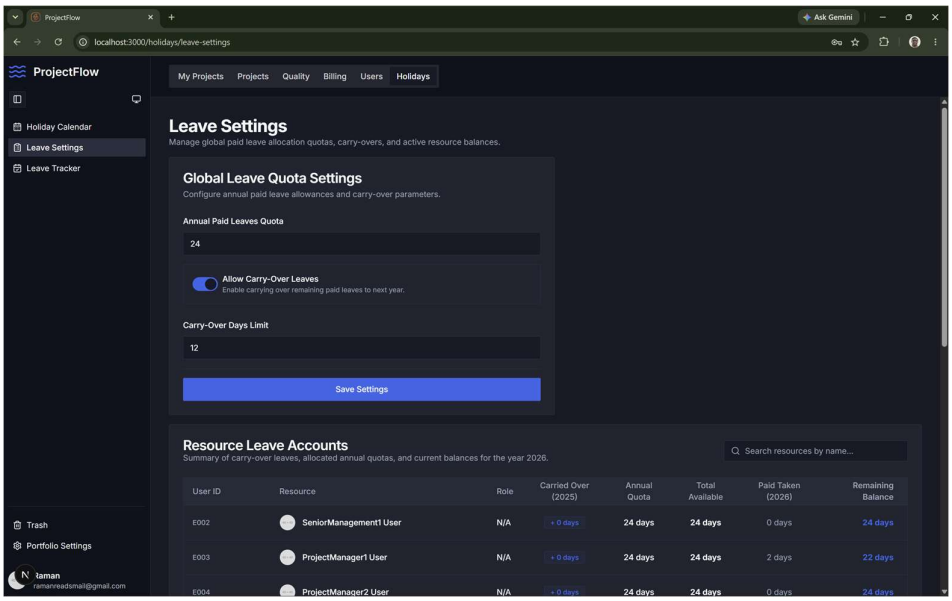

Leave Tracker


This is the place where users can apply their leaves. The leaves applied here will be automatically be reflected in the projects they are part of. (Illegal practices like taking leave in one project to work on the other are not encouraged.)

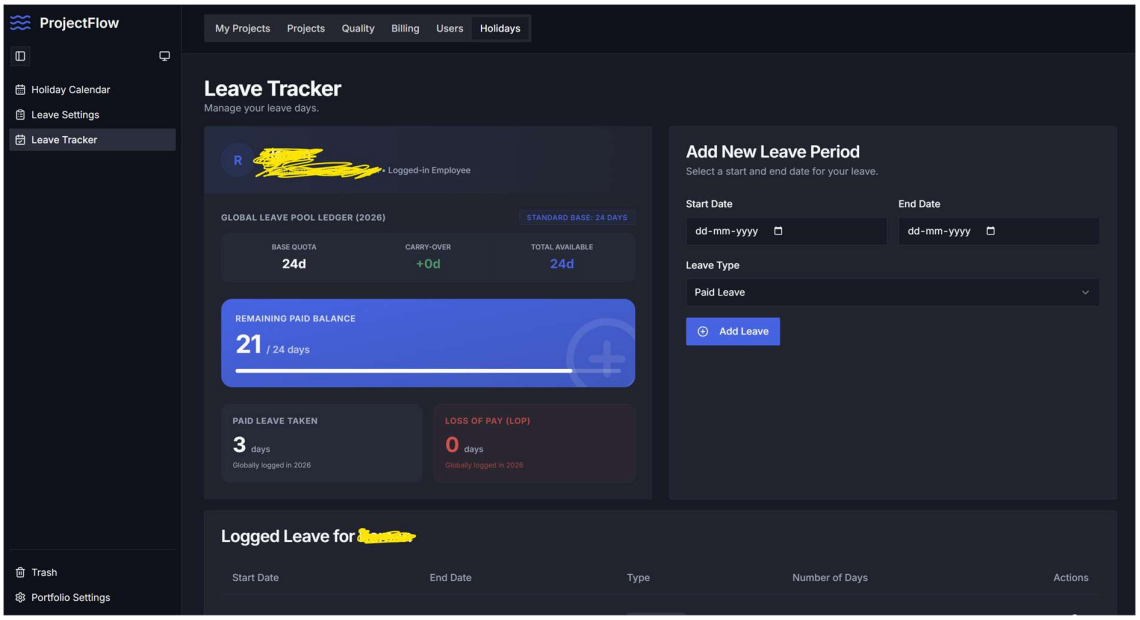

4. Initial Estimation Flow


Project Home

Add New Project. Select Initial Estimation in the project status.

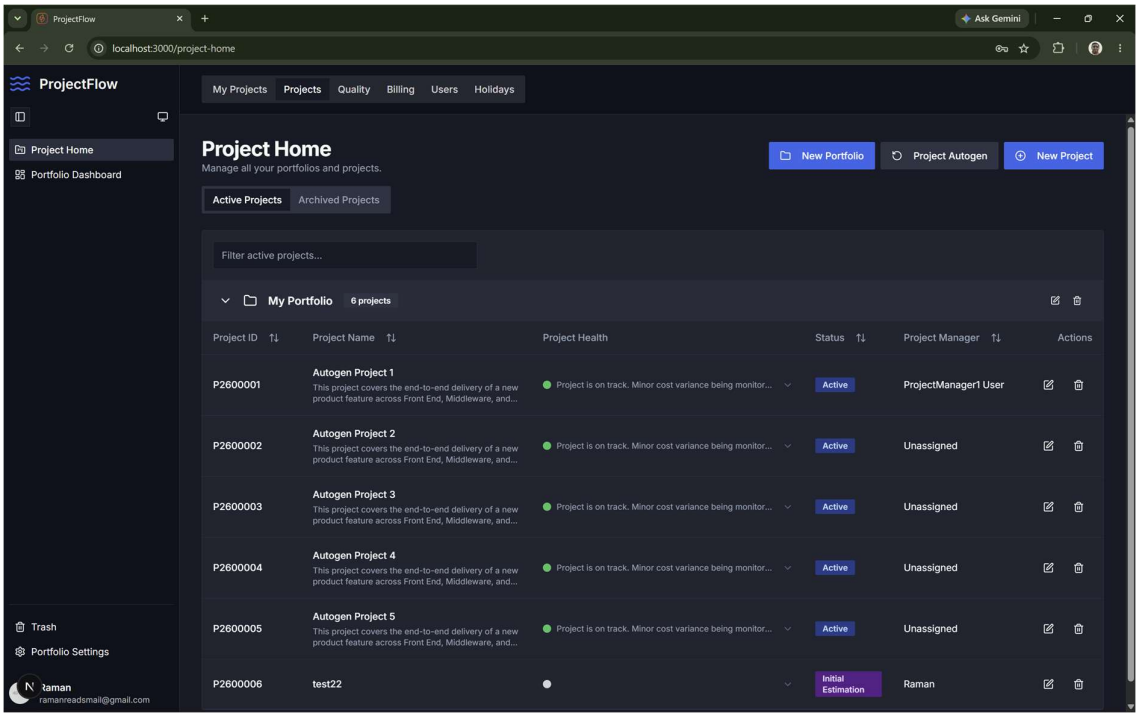


Initial Estimation


Add the project summary (sufficiently detailed) and save.

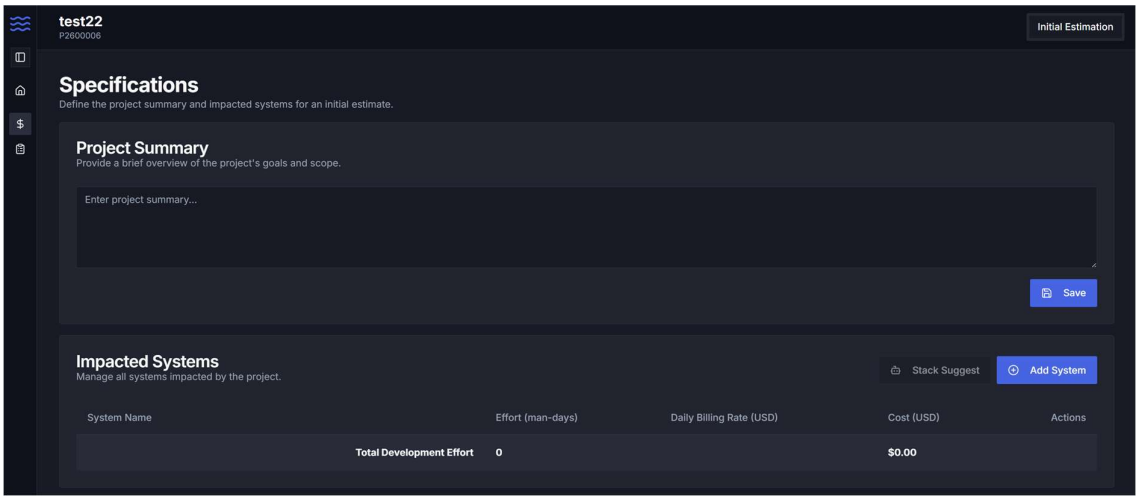

Click on the Stack Suggest button and AI will read the project summary and provide you 3 best development stacks to implement this project. You can choose one and it will be reflected under the Impacted Systems. If you do not want to use AI or add something on


your own to suggested stack, you can simply click on the Add System and create your own.

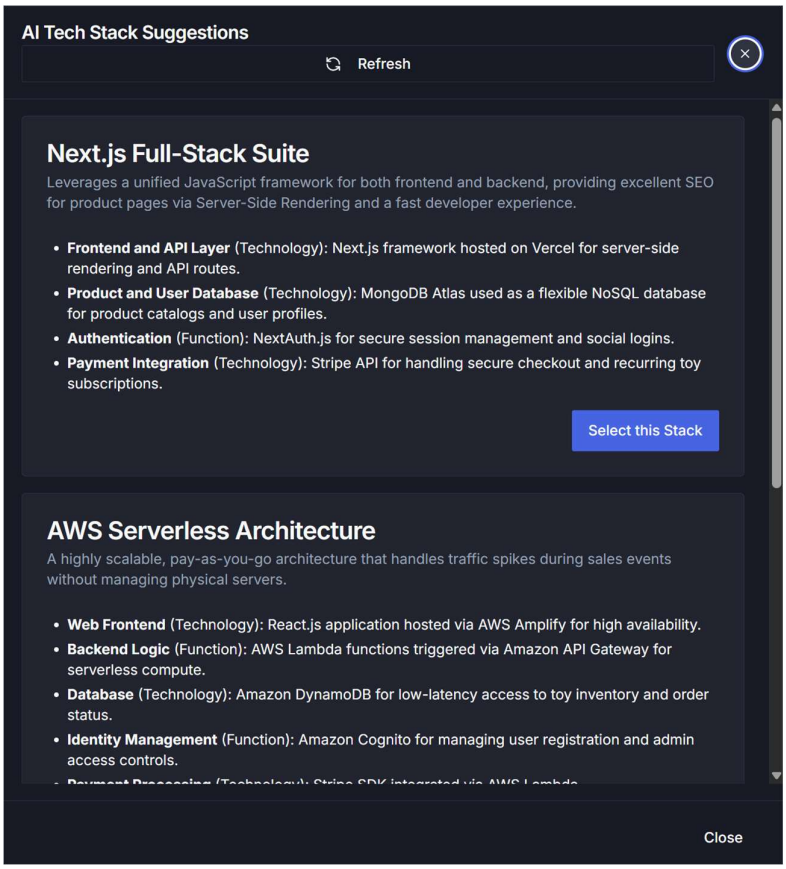


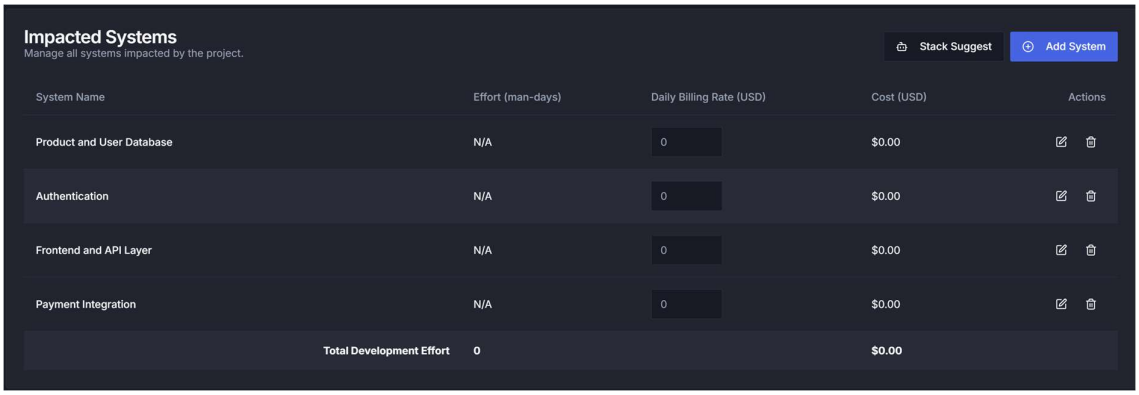


Add the daily billing rate. This will be used for calculating the invoice.


Similarly, you can add the horizontals (PM, BA, QA, Architecture, UI-UX, DevOps etc) using the AI Horizontal suggest or directly using Add Horizontal button.




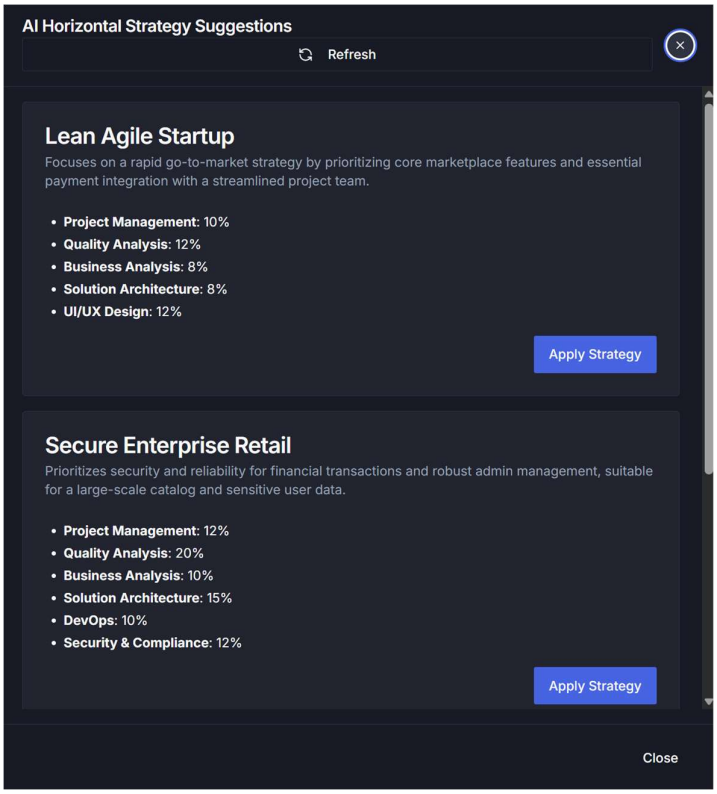

Before clicking the Confirm Estimation, use the AI Estimator button to automatically calculate the estimation. (Use this as a benchmark. AI calculates effort based on the average it has from the average it got from observing developers all over the world. Your team skill might differ and hence the estimate might be higher or lower. Adjust accordingly.)

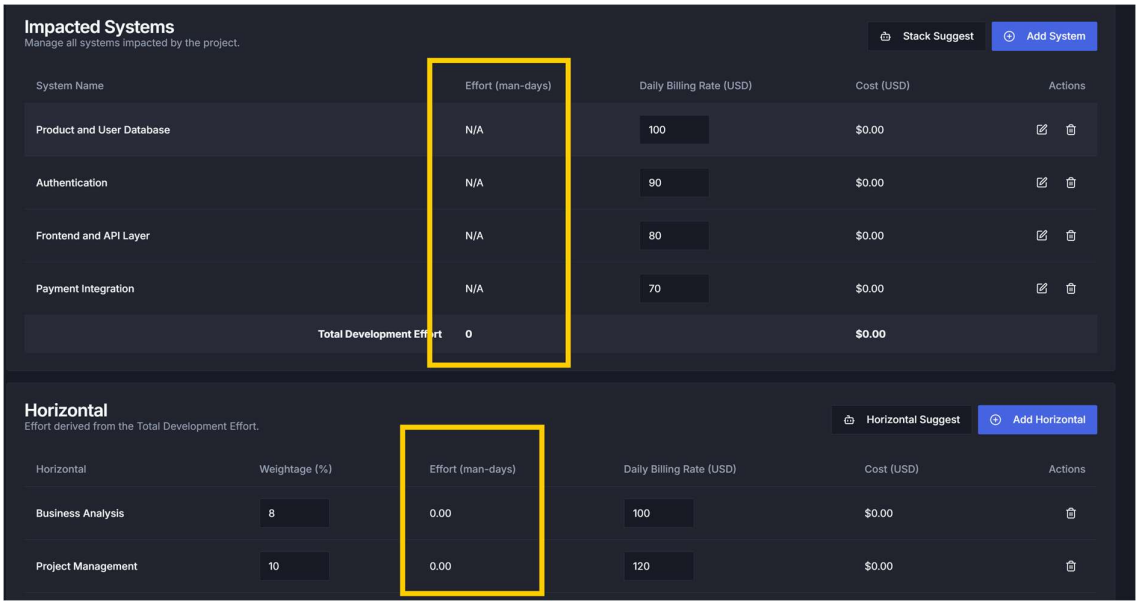
Impacted Systems
Manage all systems impacted by the project.
Stack Suggest
Add System
System Name
Effort (man-days)
Daily Billing Rate (USD)
Cost (USD)
Actions
Product and User Database
N/A
100
$0.00
Authentication
N/A
90
$0.00
Frontend and API Layer
N/A
80
$0.00
Payment Integration
N/A
70
$0.00
Total Development Effort
0
$0.00
Horizontal
Effort derived from the Total Development Effort.
Horizontal Suggest
Add Horizontal
Horizontal
Weightage (%)
Effort (man-days)
Daily Billing Rate (USD)
Cost (USD)
Actions
Business Analysis
8
0.00
100
$0.00
Project Management
10
0.00
120
$0.00

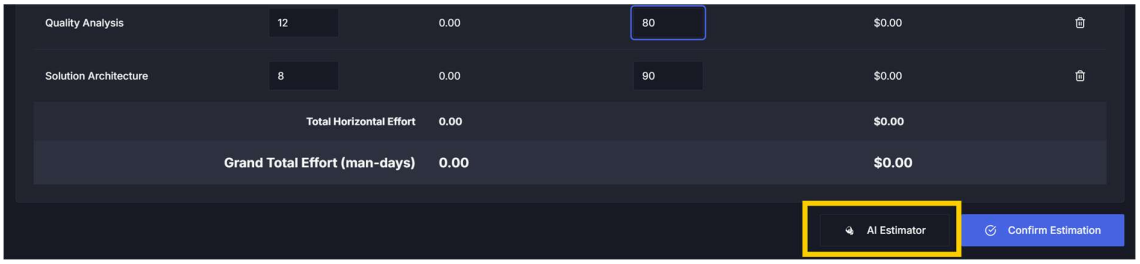
Quality Analysis
12
0.00
80
$0.00
Solution Architecture
8
0.00
90
$0.00
Total Horizontal Effort
0.00
$0.00
Grand Total Effort (man-days)
0.00
$0.00
AI Estimator
Confirm Estimation

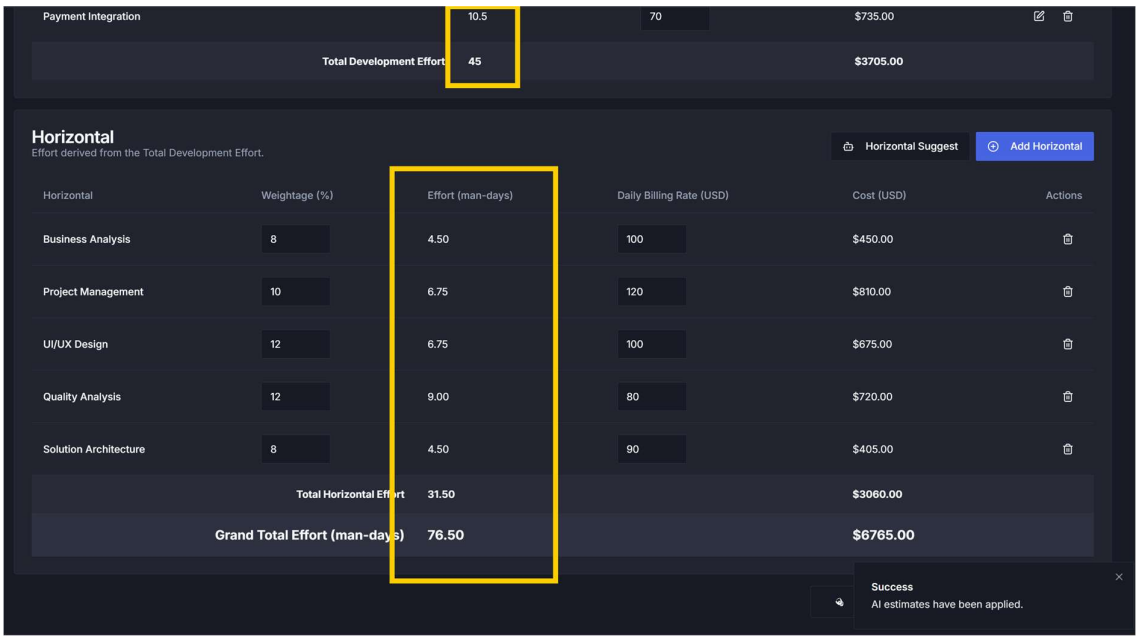

Payment Integration
10.5
70
$735.00
Total Development Effort
45
$3705.00
Horizontal
Effort derived from the Total Development Effort.
Horizontal Suggest
Add Horizontal
Horizontal
Weightage (%)
Effort (man-days)
Daily Billing Rate (USD)
Cost (USD)
Actions
Business Analysis
8
4.50
100
$450.00
Project Management
10
6.75
120
$810.00
UI/UX Design
12
6.75
100
$675.00
Quality Analysis
12
9.00
80
$720.00
Solution Architecture
8
4.50
90
$405.00
Total Horizontal Effort
31.50
$3060.00
Grand Total Effort (man-days)
76.50
$6765.00
Success
AI estimates have been applied.

5. Project Flow

Project Details

Project Status

This is the page where you can edit the basic project details and the project health. We select the pricing model (FB or TnM) here. It is important to select the pricing model because the billing calculations depend on the pricing model.

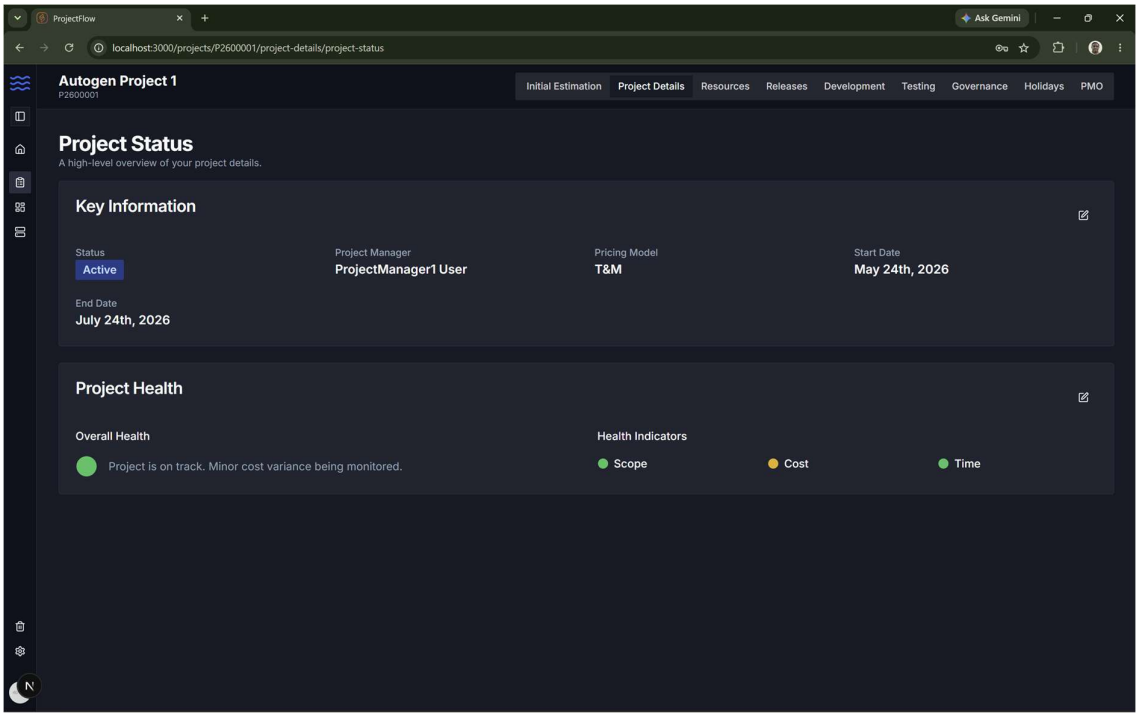


PM Dashboard

This Dashboard page is designed for the view of the PM upwards. This tracks the overall progress of the project both sprint and release wise. It can also show the progress of the different stories Epic wise if there are multiple epics involved.

The time section shows the total effort taken for the sprint/release as per plan (estimation) as per worklog (what the team member has put in) and derived as per the movement of the ticket in the Kanban.

The Workload section shows the total effort each resource has put in for development for that sprint. It will not only show the story/task hours, but also the bug fixing hours. This can be used to understand the quality of the development work. The more time spent towards bug fixing generally means the original work was not thought through.

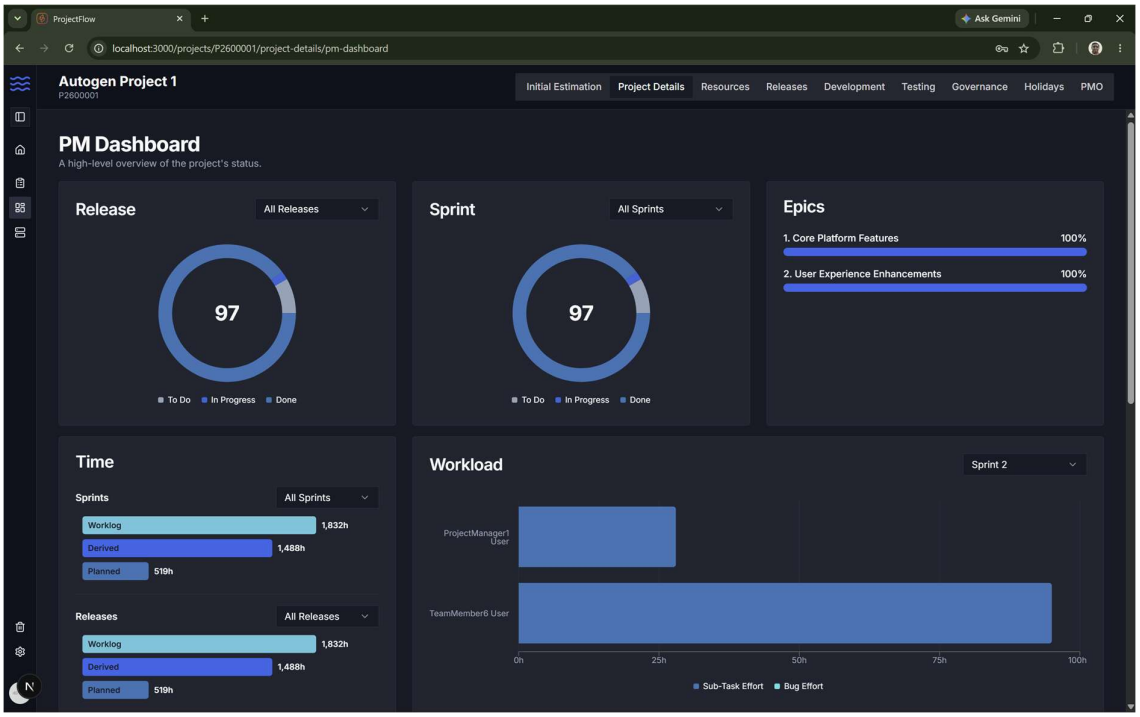


Resource Cost section shows the billed vs actuals for each type of resource.

Fixed Cost shows a comparison of how much was spent for different fixed costs.


Time spent by swim lane helps in identifying if there are any bottlenecks in the flow. Expectation is to have enough swim lanes to cover each handover.

Time by Resource shows the average time a story/task takes with each resource. This helps in identifying if a resource is overloaded or needs help.

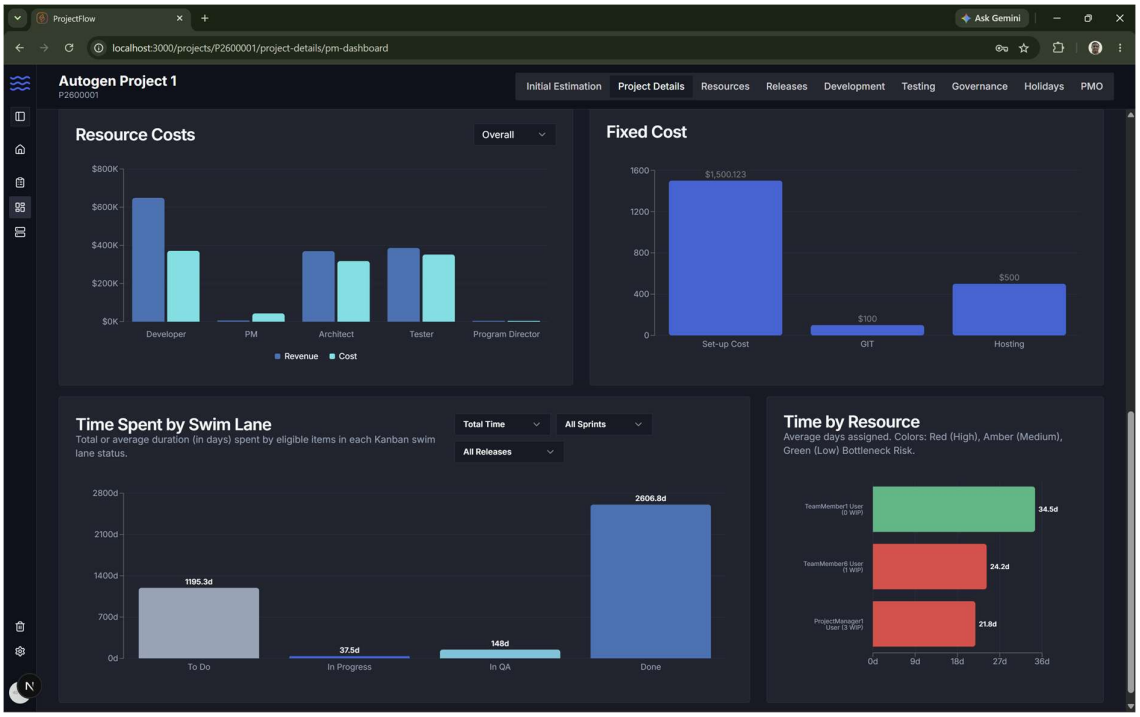

Specifications


Sections same as Initial Estimation with addition to Environment Details




Resources

Project Resources

Adding a resource is basically selecting a resource from the global user pool. While adding make sure that the resource's capability is mapped to one of the impacted systems. If you team follows full stack development, make sure full stack development is added as an impacted system in Specifications page.

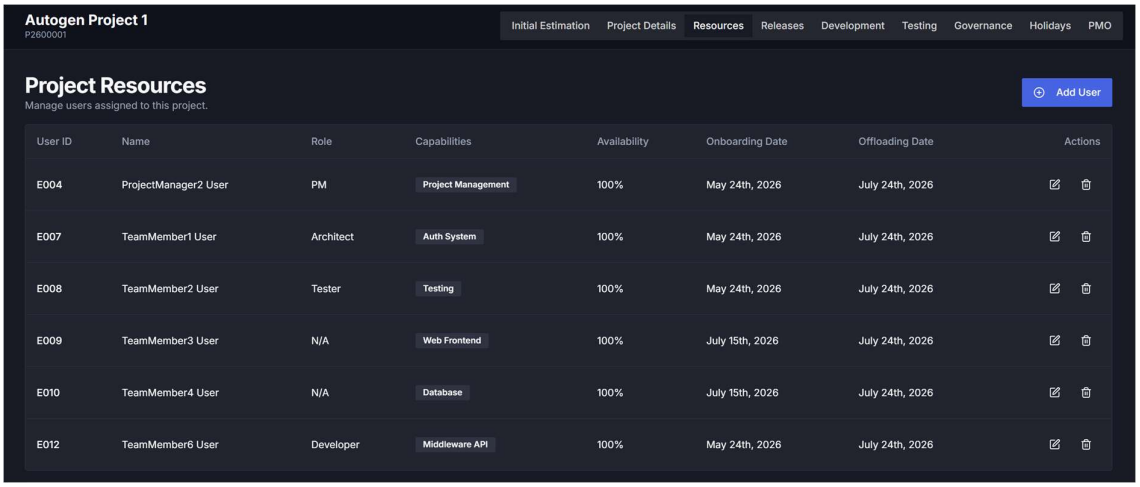


This section helps in identifying you team's total capacity for a sprint/release impacted system wise.

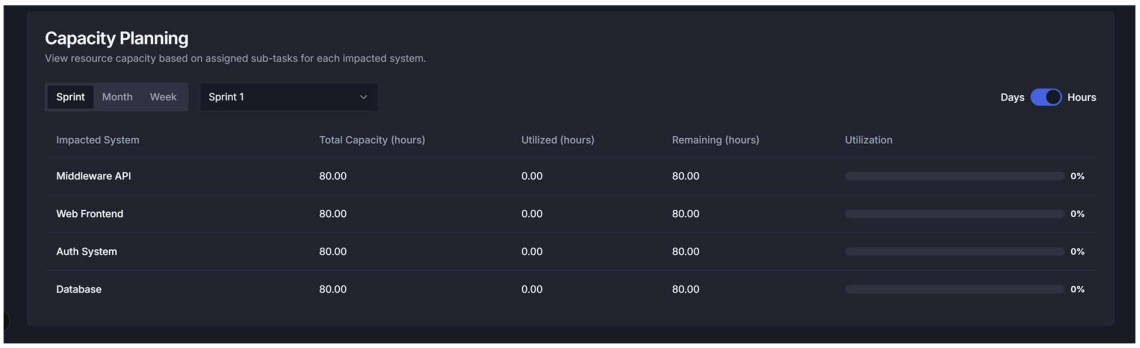


Worklog

In this page, the resources can enter their daily work hours against the story/task/activity they worked on. If the activity is not in the list, they can select Other and describe the activity.

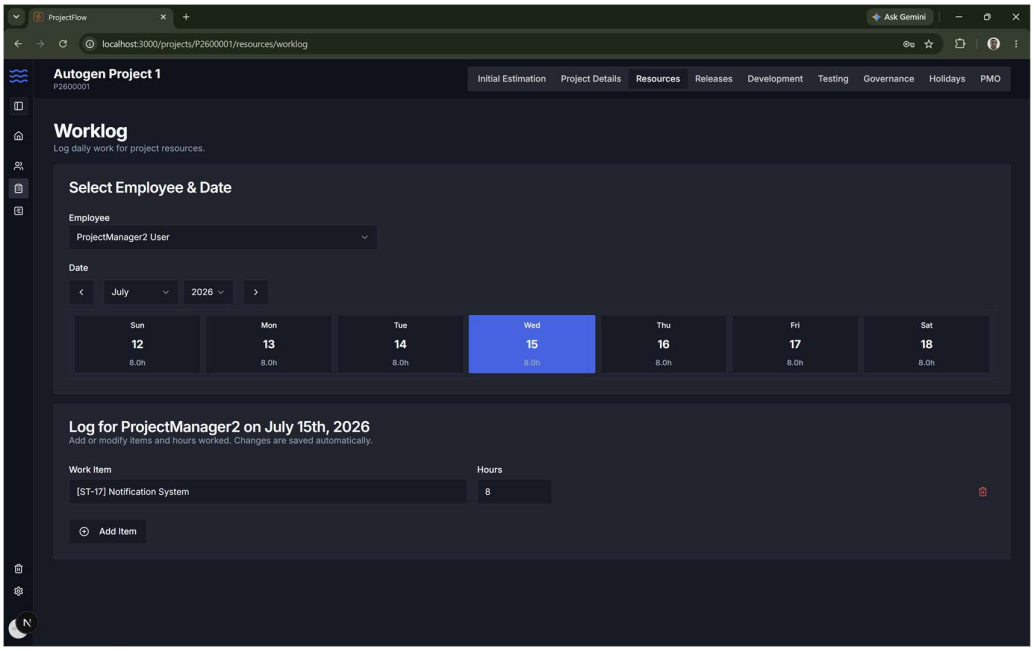


Resource Workload

This page is intended for PM upwards to see the workload of resources, check if they are over or under loaded.

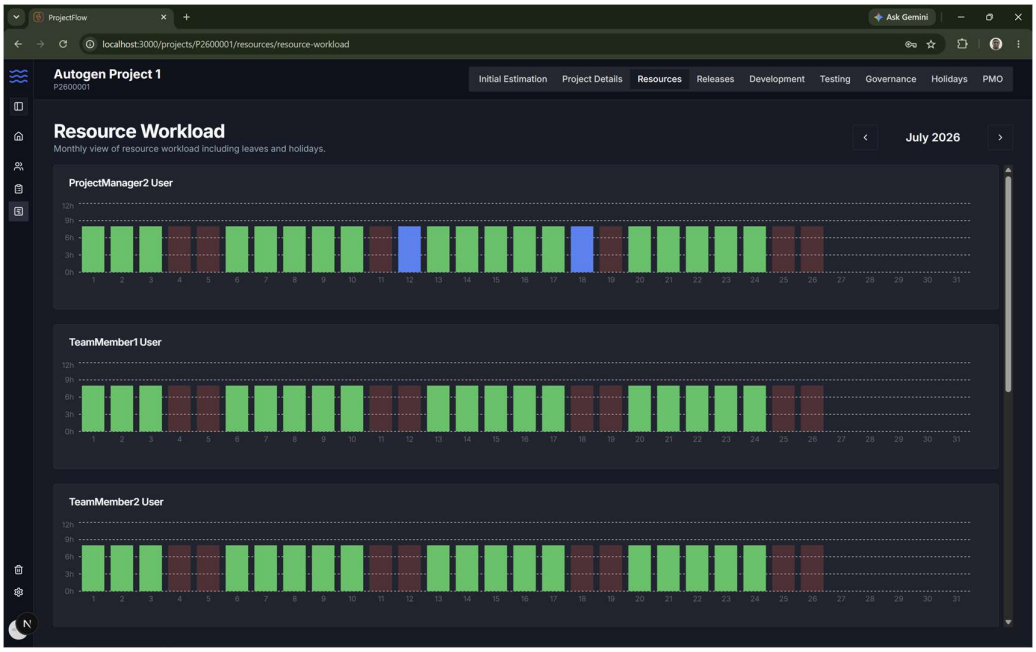

Releases


This page is used for those hybrid projects where development happens with fixed scope and budget but overall delivery has to be in agile to an enterprise client who follows release/release trains.

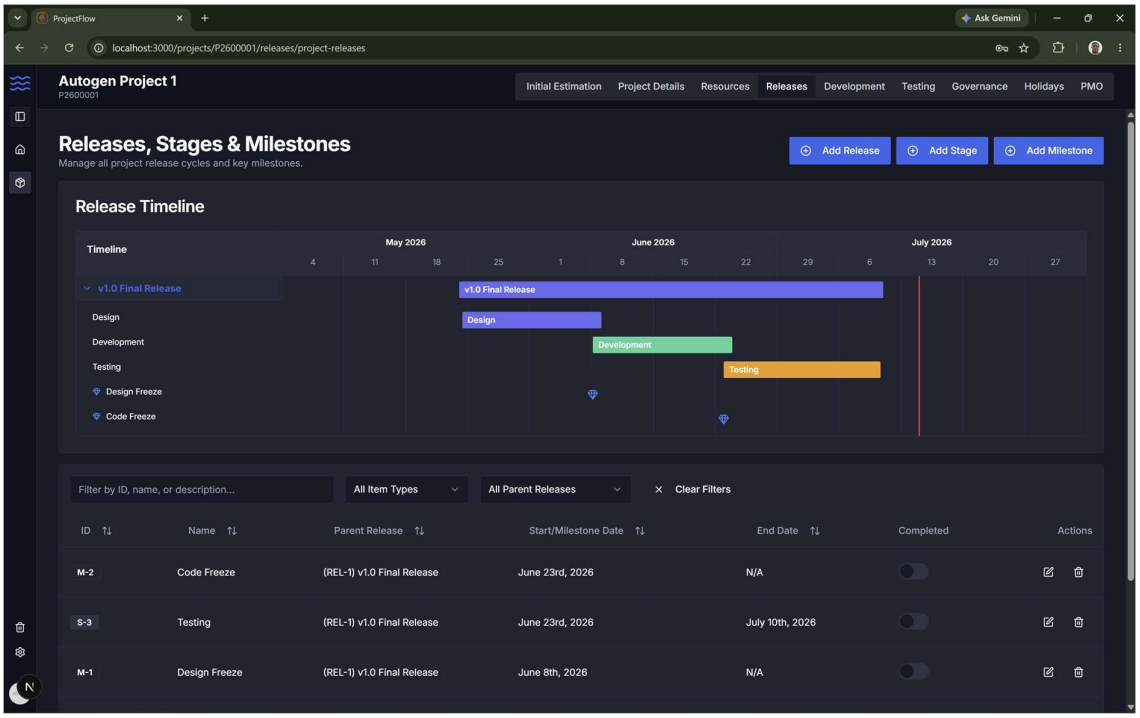

Development

Development Dashboard

This page is for the team to track their overall status using the sprint burndown and release burnup charts

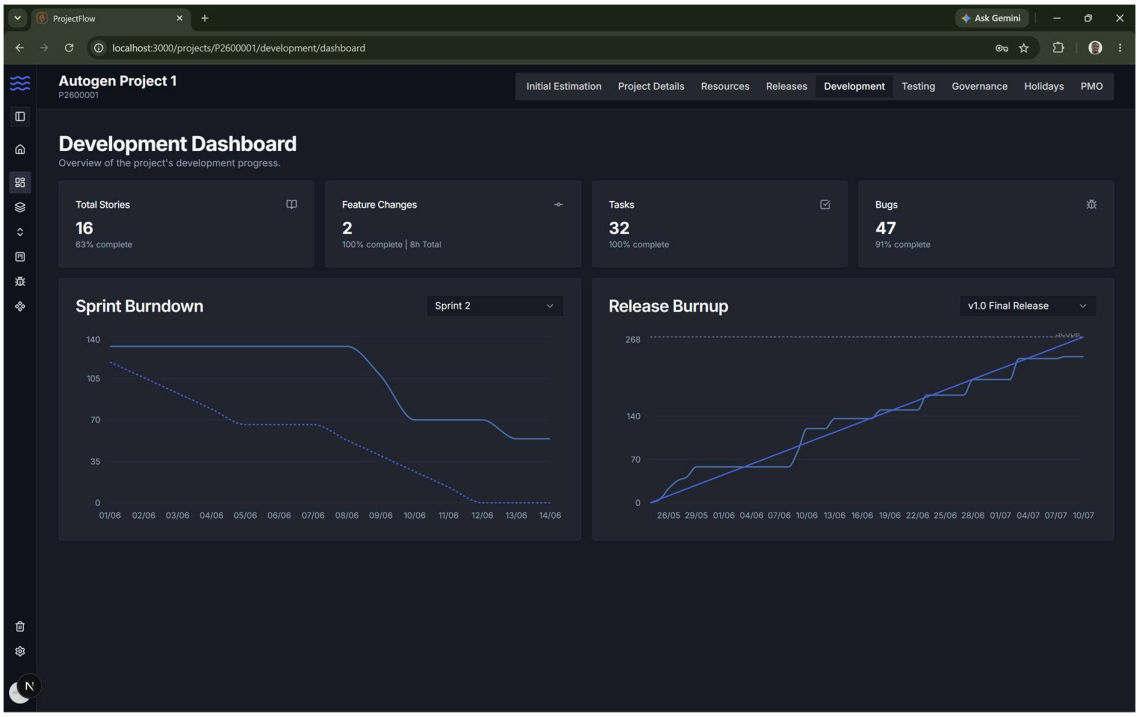

Product Backlog


Here you can add stories/tasks/feature changes/bugs(which are not related to stories) directly to the product backlog. Epics are used to group them. Best practice is to have every story under an Epic and not unassigned.


General flow is the Product Owner/Business Analyst will create the story in the backlog. After that the Tech Lead will go through the stories and identify the impacted systems. Post that the Lead along with the developers will elaborate the story by writing a sub-task for each impacted system and provide an estimation (either in hours or days). The sum of the efforts of the sub-tasks will be the total effort of the story.


In case of full stack dev teams, there is no need for sub-tasks. The effort can be given at story level.

Note – ProjectFlow team acknowledges the fact that agile community prefers to give estimations in story points which are generally not tied to standard time (like hours or days). But it also acknowledges the fact that work is expected to be delivered on fixed dates and sometimes deadlines are immutable. And work gets billed based on that. For years now Project Managers and Scrum Masters world-wide have struggled with the

conversion of story points to hours. In the Project Settings, there is an option to convert the story points to hours. We have also given the shortcut for converting.

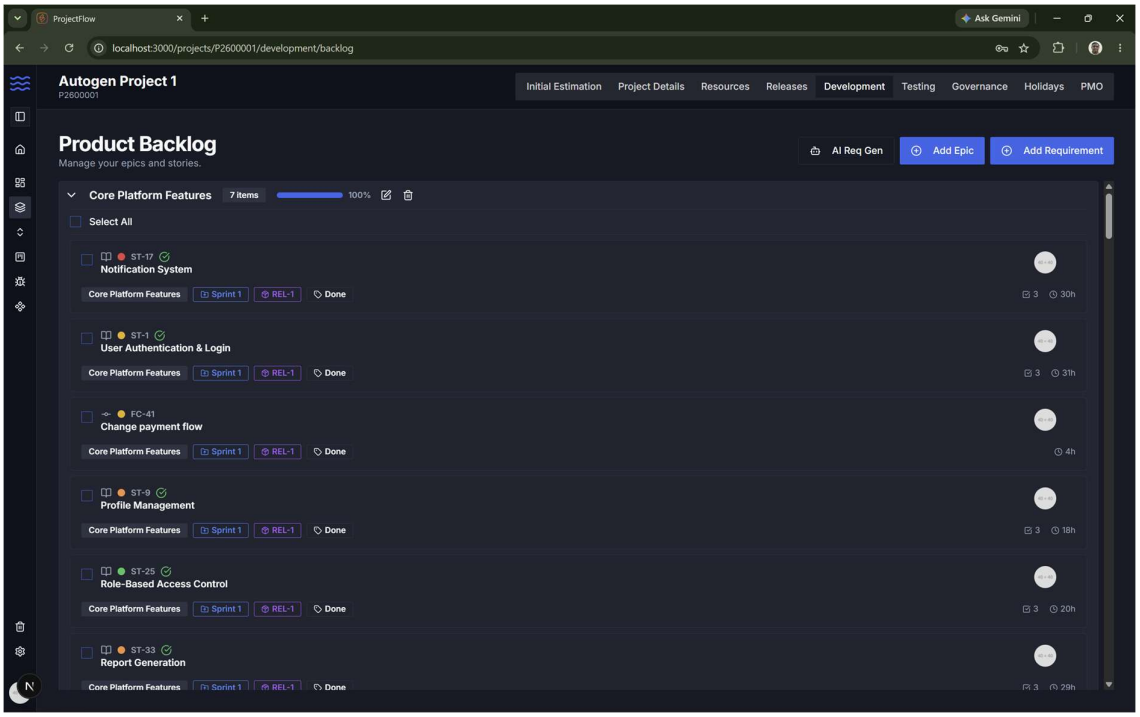





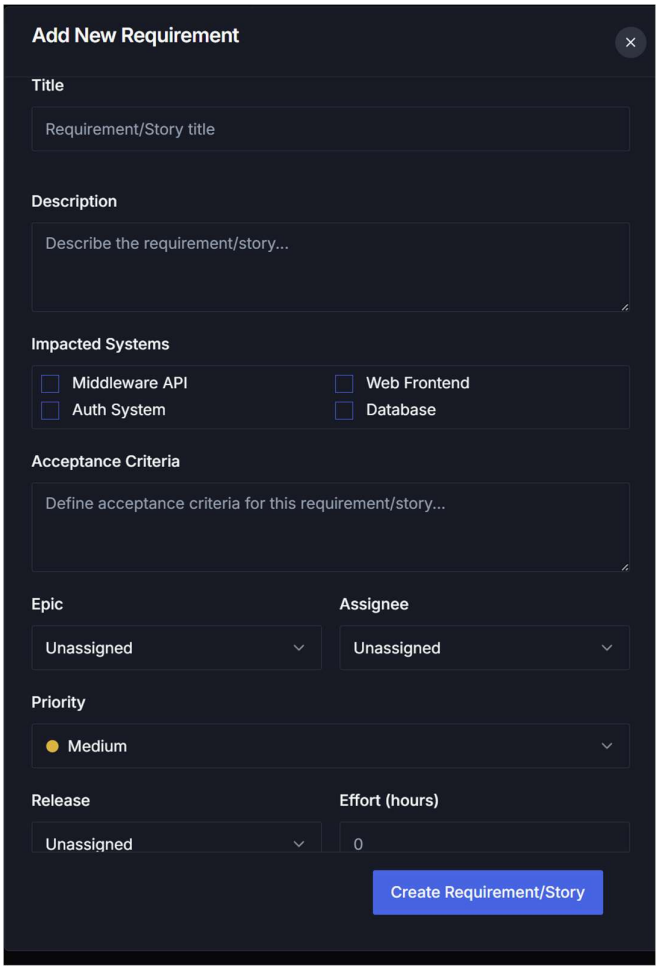
Add New Requirement
Title
Requirement/Story title
Description
Describe the requirement/story...
Impacted Systems
Middleware API
Web Frontend
Auth System
Database
Acceptance Criteria
Define acceptance criteria for this requirement/story...
Epic
Unassigned
Assignee
Unassigned
Priority
Medium
Release
Unassigned
Effort (hours)
0
Create Requirement/Story

Sub-Tasks


Though Sub-Tasks can be created in the Product backlog itself by editing the story and selecting the sub-task tab and adding it there, taking into consideration the difficulty that the Tech Leads and Managers face in assigning this to developers, this page was made to help them assign sub-tasks in bulk. This also gives a view to see if any are left un-assigned.

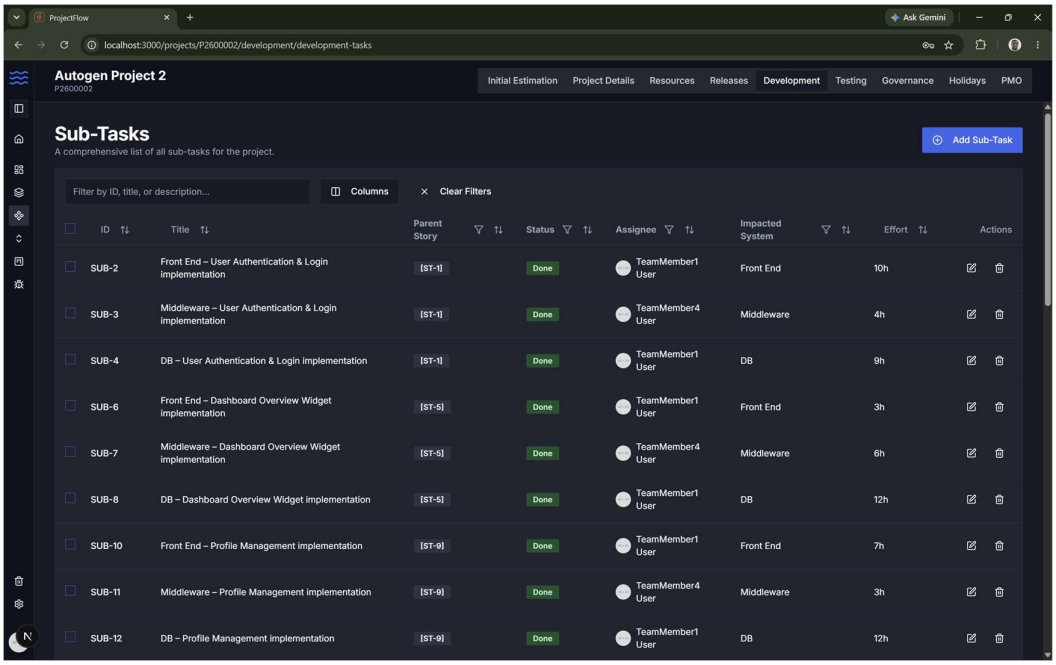


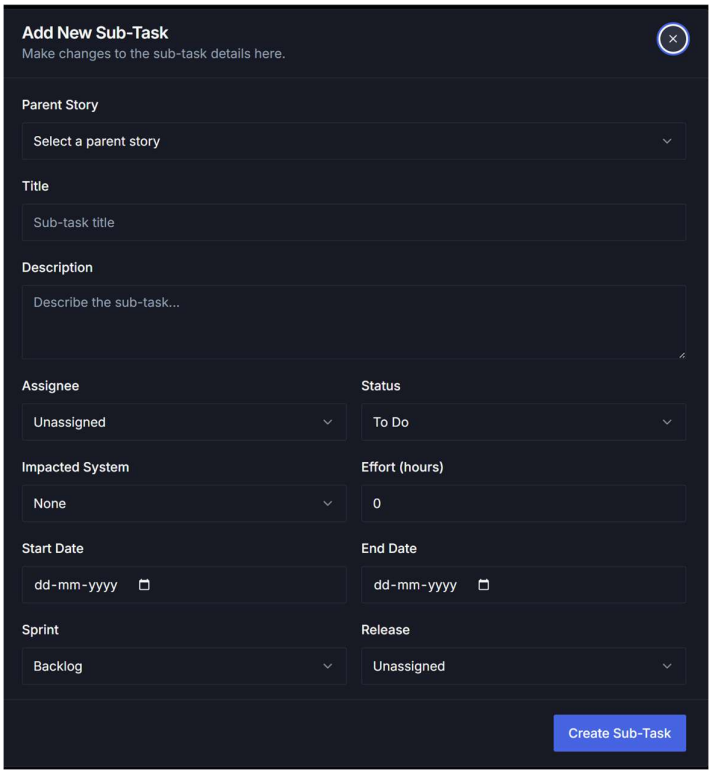


Grooming

Grooming board shows the Product Backlog items in the left column. User can create sprint in the right column. The stories which are ready (the ones with green tick mark, meaning there is at least one subtask with effort for each impacted system are defined ready) can be moved to a sprint. The bars on the top shows the utilized capacity. This will help the Project Manager/Scrum Master to stop adding tasks when the critical path is reached.

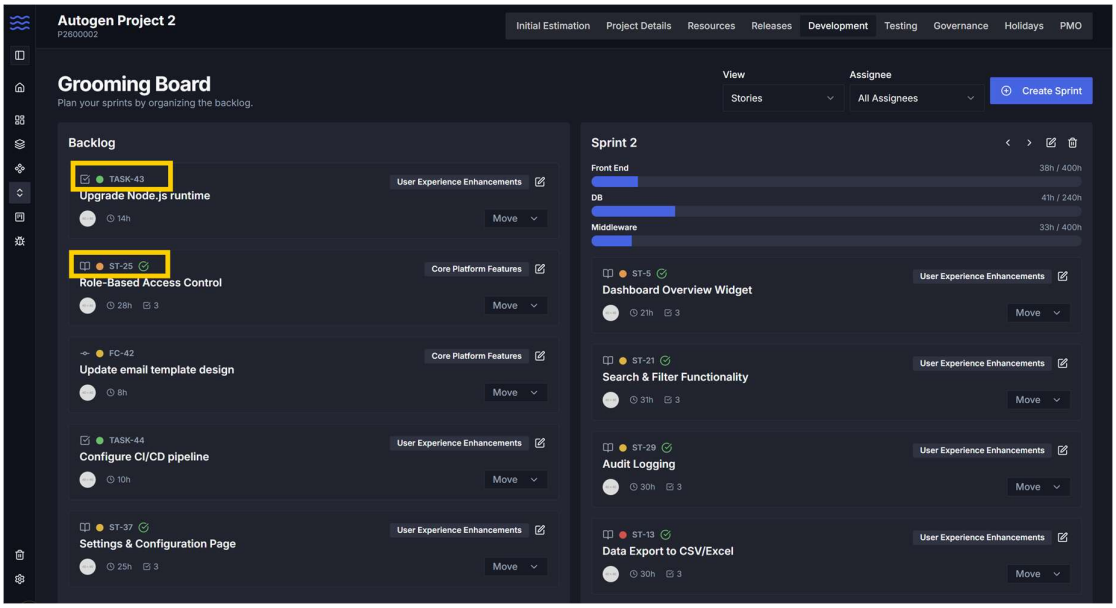


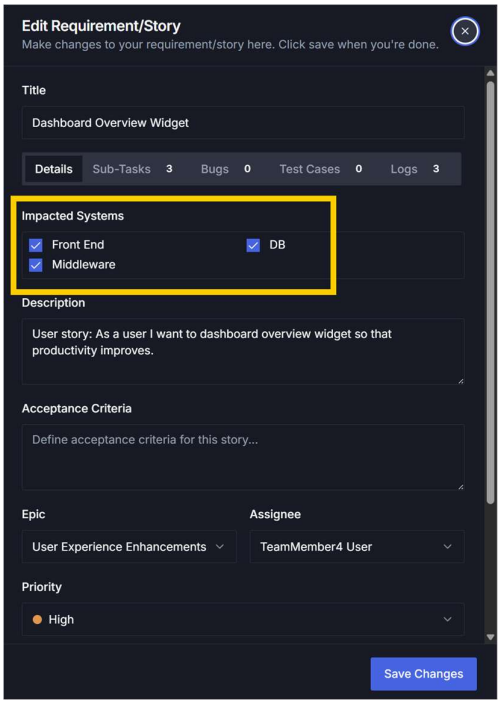


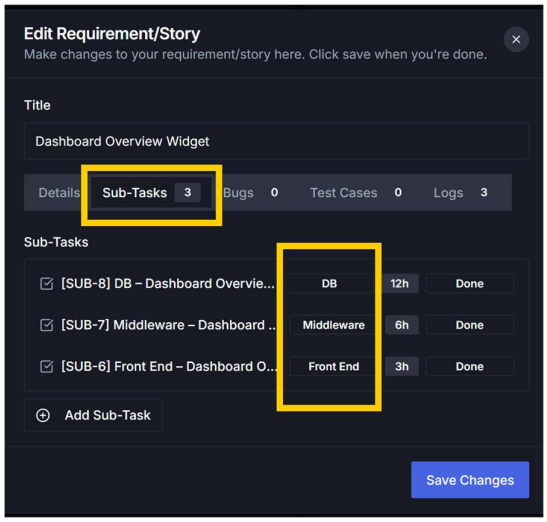

Kanban Board

The board not only provides regular story view, user can also view based on sub-tasks. The tickets can also be filtered based on assignees.

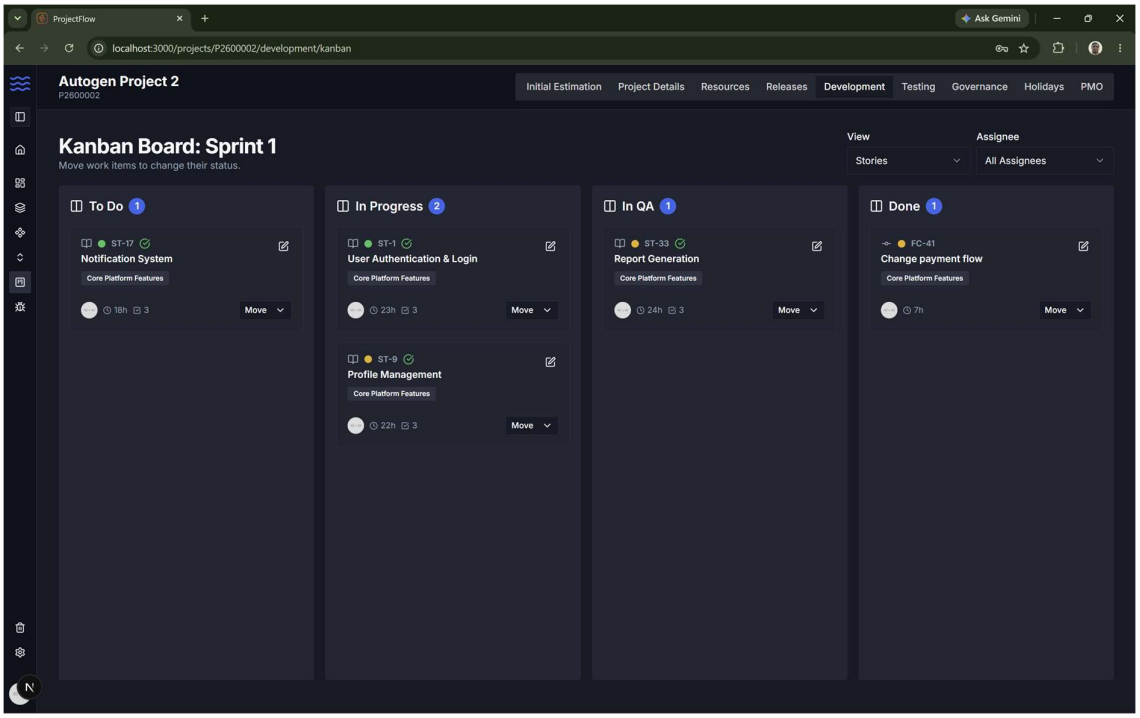

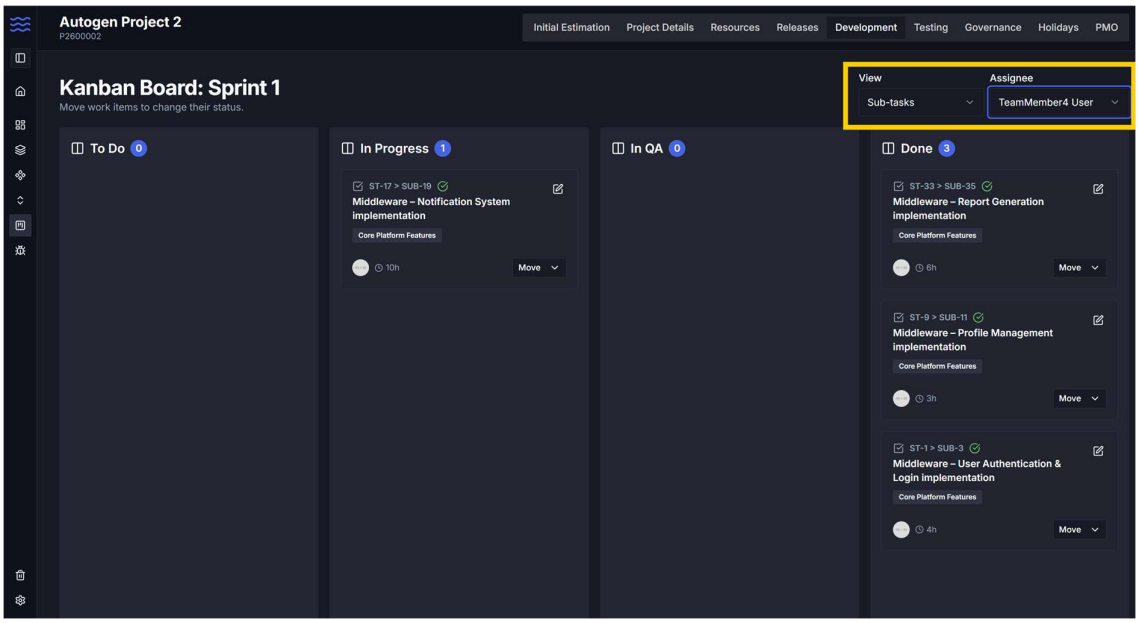

Testing

Testing Dashboard


This dashboard shows the status of test case execution, bug status and bug severity filtered by Test Plan (SIT, UAT, PROD etc.)

The Daily view shows the number of test cases to be executed for that day, test cases actually run and the number successfully closed. This will show once the test plans are created and test cases assigned for each day of the test plan. The second graph shows the number of bugs opened on each day of test execution.




Test Leakage shows the total number of bugs on each Test Plan run by severity.

Story Test Coverage shows what percentage of the stories are covered by the test cases.

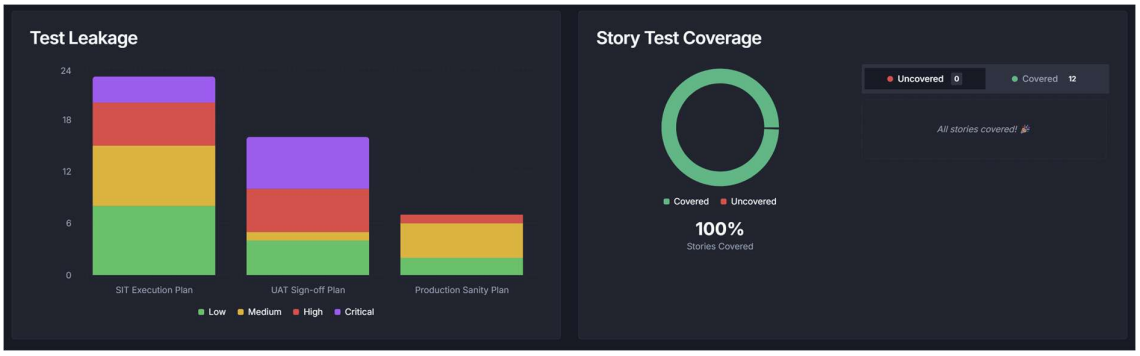


Test Backlog

Test Backlog contain the complete list of test cases created for the project.

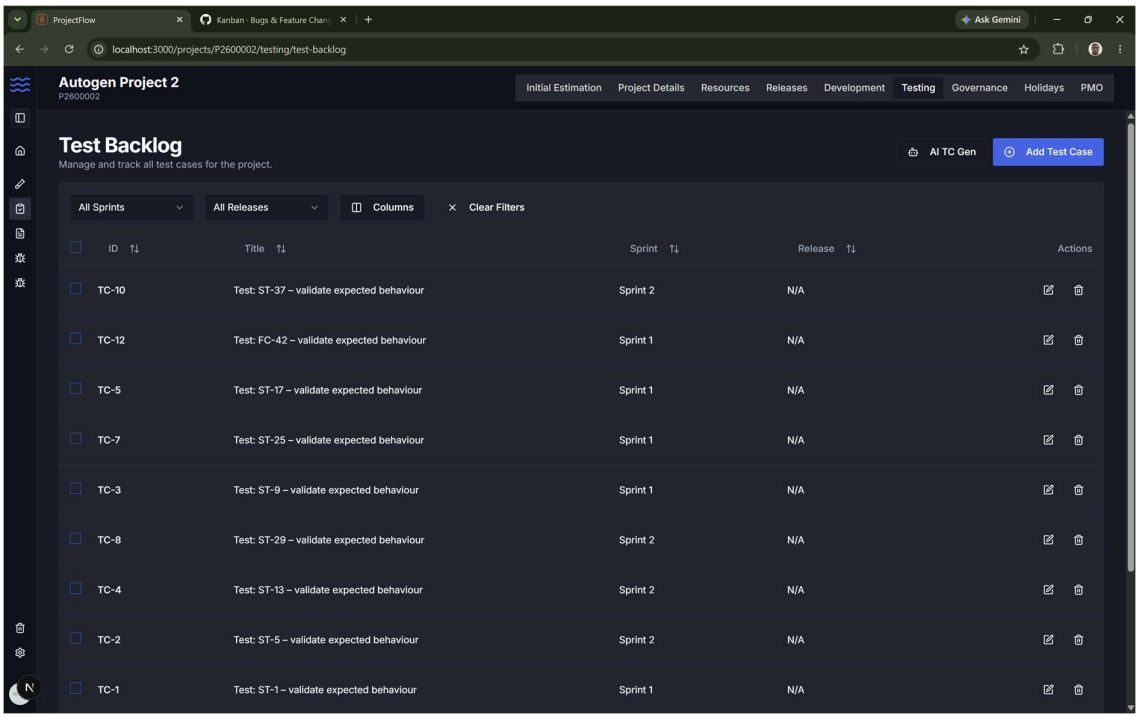


Test Plan


When a test plan is created, test cases from the backlog are copied to the plan.

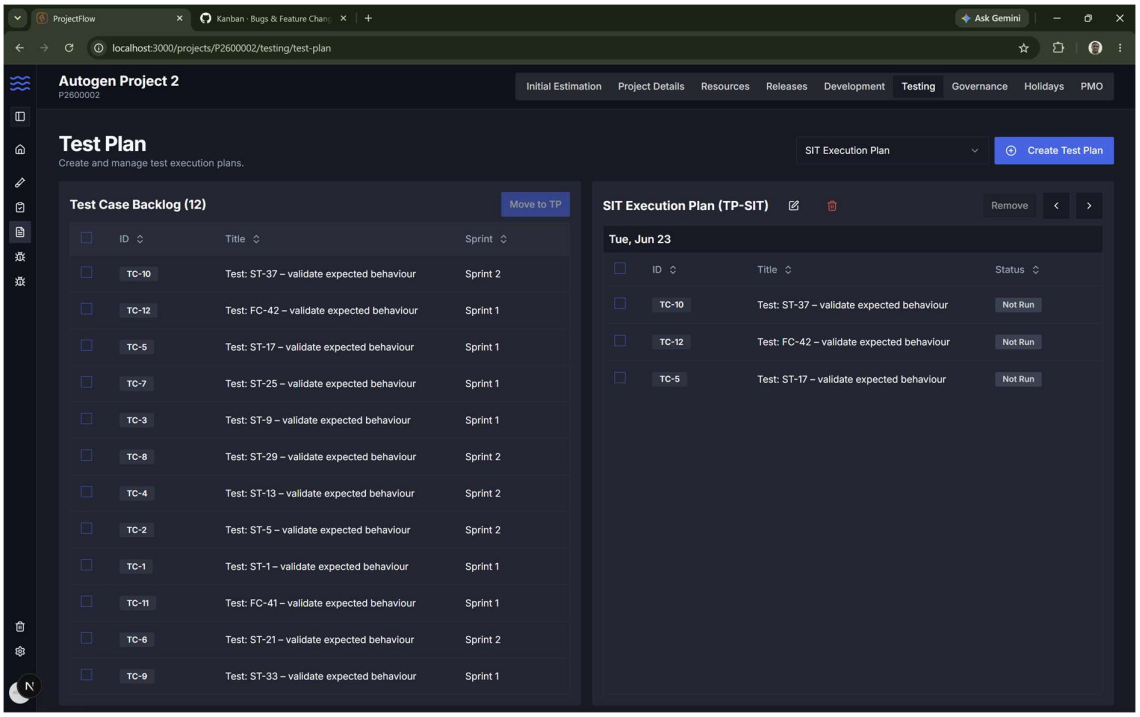

Defects


The testing team can log their defects in this page. Once the story id is given, they are automatically mapped inside the story card.

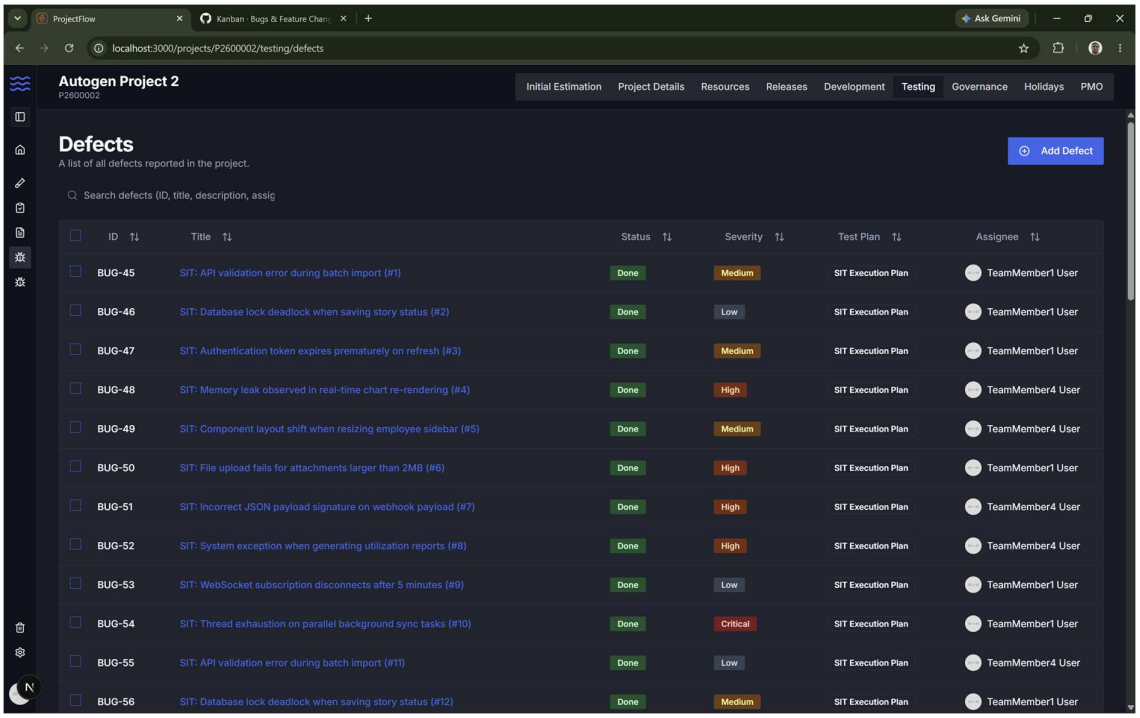

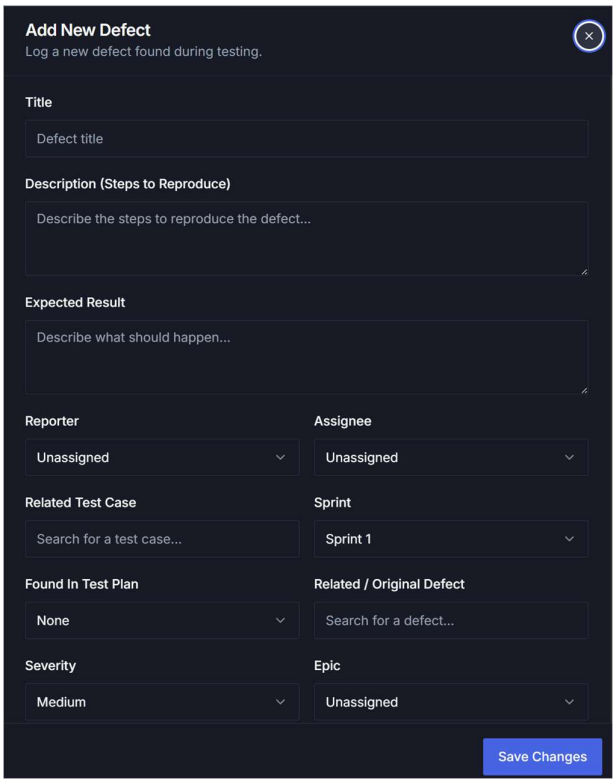

Defect Tracker


This board is exclusively to track the status of bugs by release/sprint/test plan.

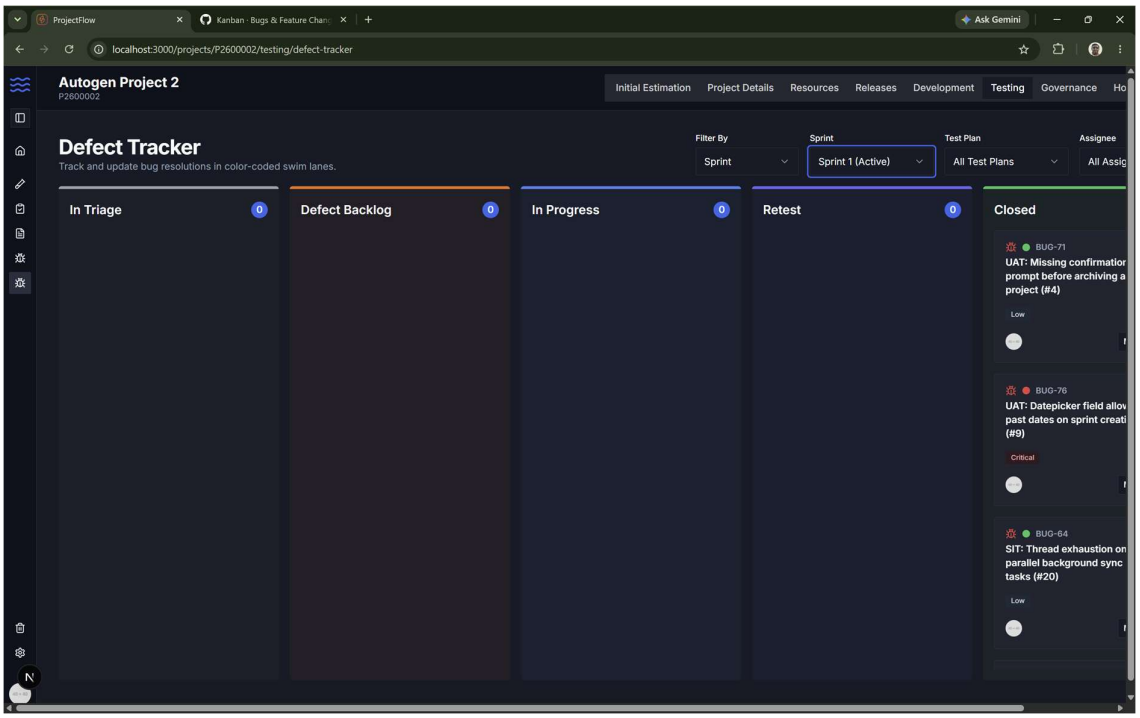

Governance


RAID Dashboard

RAID (Risk, Assumption, Issue, Dependency) Dashboard captures the overall status of the RAID items.

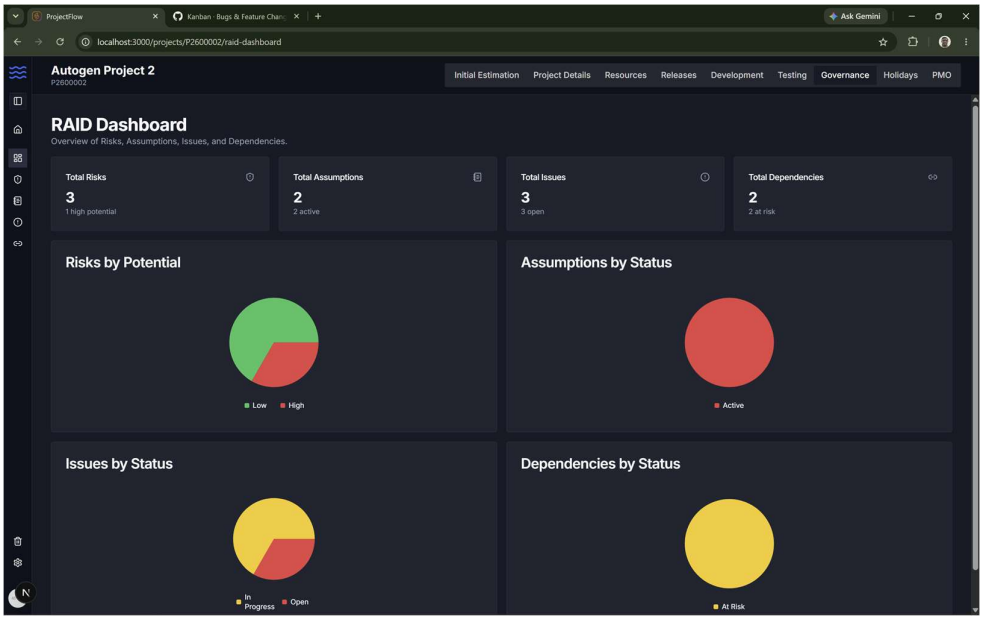


Risks

Captures the Risks. AI Risk Generator button will invoke the AI to go through the project and identify risks that are common across similar projects. User can add their own risks by clicking the Add Risk button.

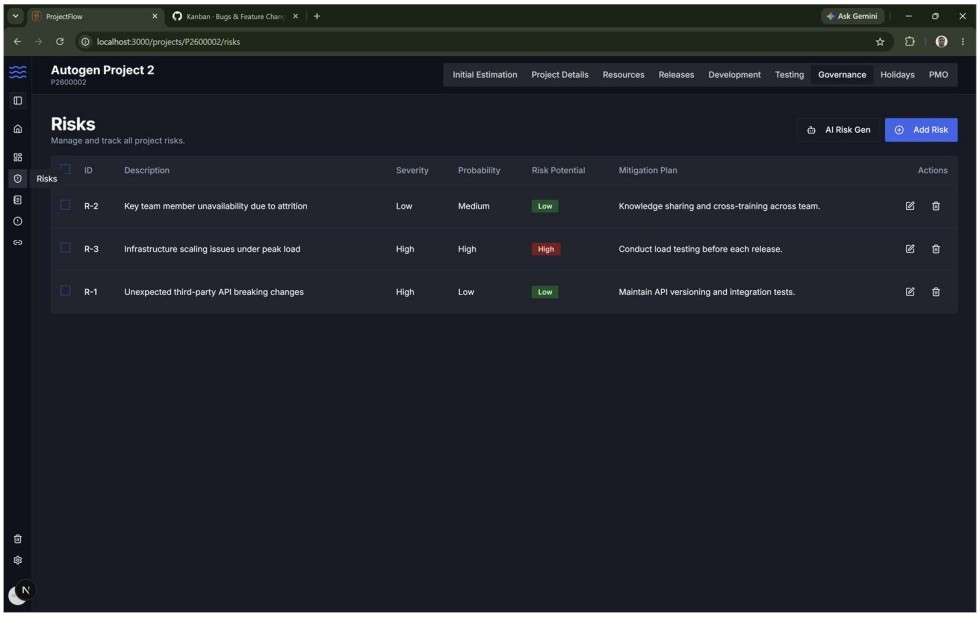


Assumptions

Captures the Assumptions made during requirement, analysis, design phases. AI Gen Assumptions calls AI to verify the requirements and generate a list of assumptions made. User can add their own assumptions by clicking Add Assumptions button.

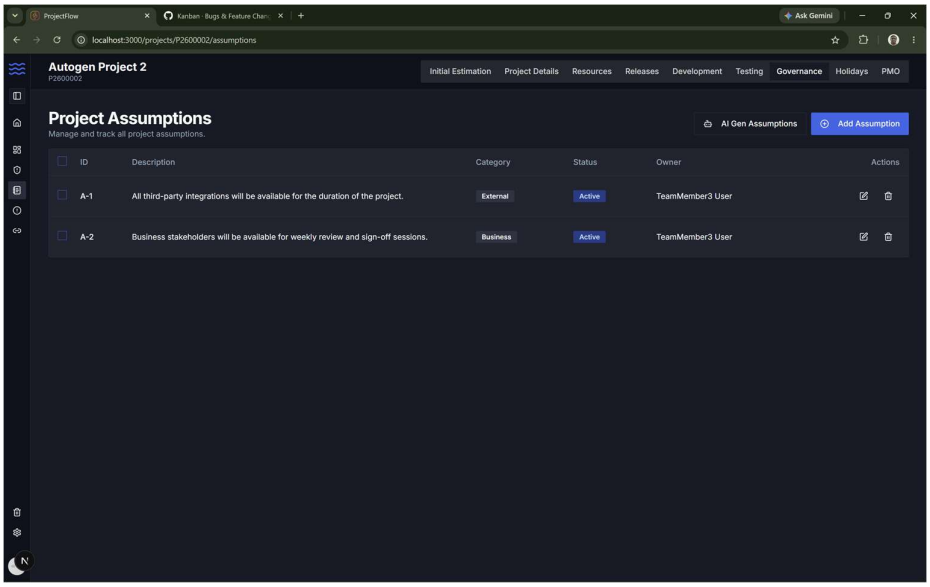


Issues

This page lists the project operational issues, not to be confused with the development bugs. Usually these are risks which have materialized.

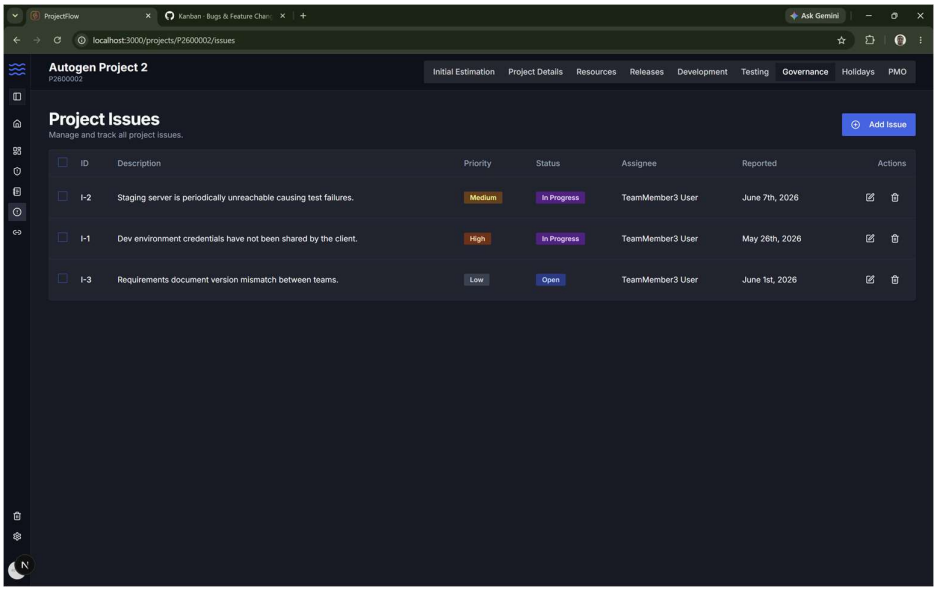

Dependencies


Captures the third-party dependencies the team has to complete their delivery. AI Gen Dependencies will make the AI check the requirements and point out the dependencies. User can also add their own dependencies.

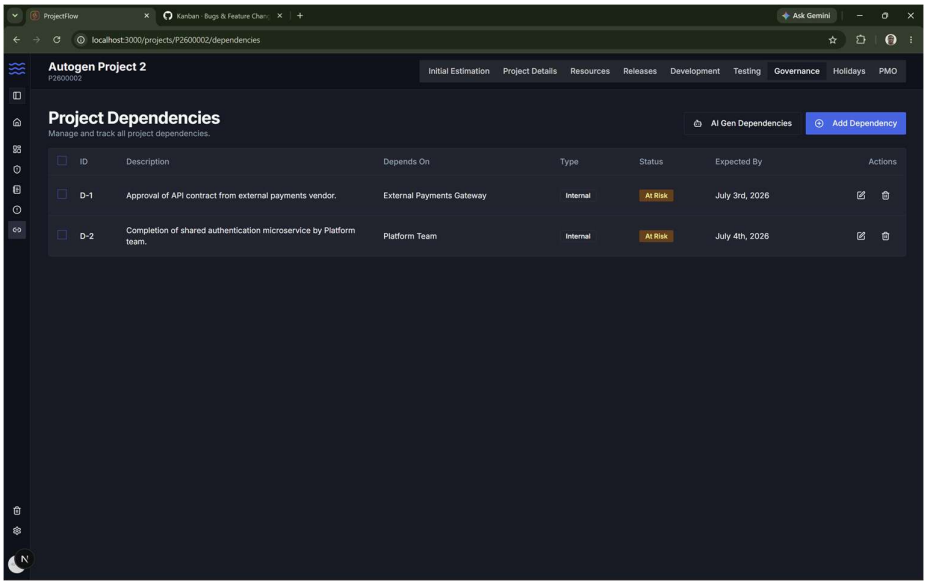

Holidays

Holiday Calendar


This page is for the PM upwards to override the global holiday settings if the particular project follows a different time zone.

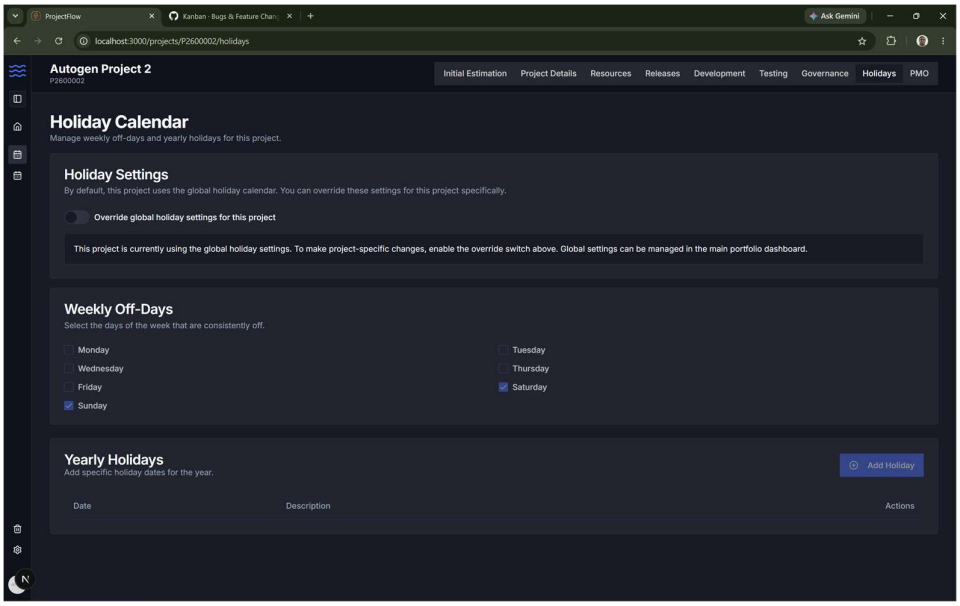

Leave Calendar


Leave Calendar

This view is for PM upwards to see which are team members are on leave on a particular day. This can help them in identifying potential resource crunches.

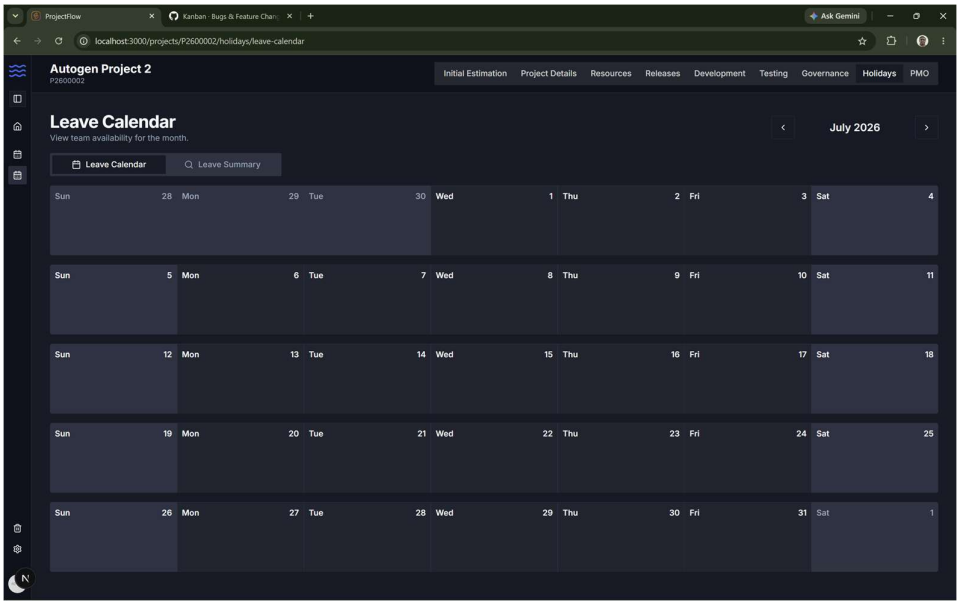

Leave Summary

Lets the Manager view the overall leave availability for the team members and the number of Loss of Pay leaves each member has taken. This is to make sure billing reflects the LOP days when the client requires it.

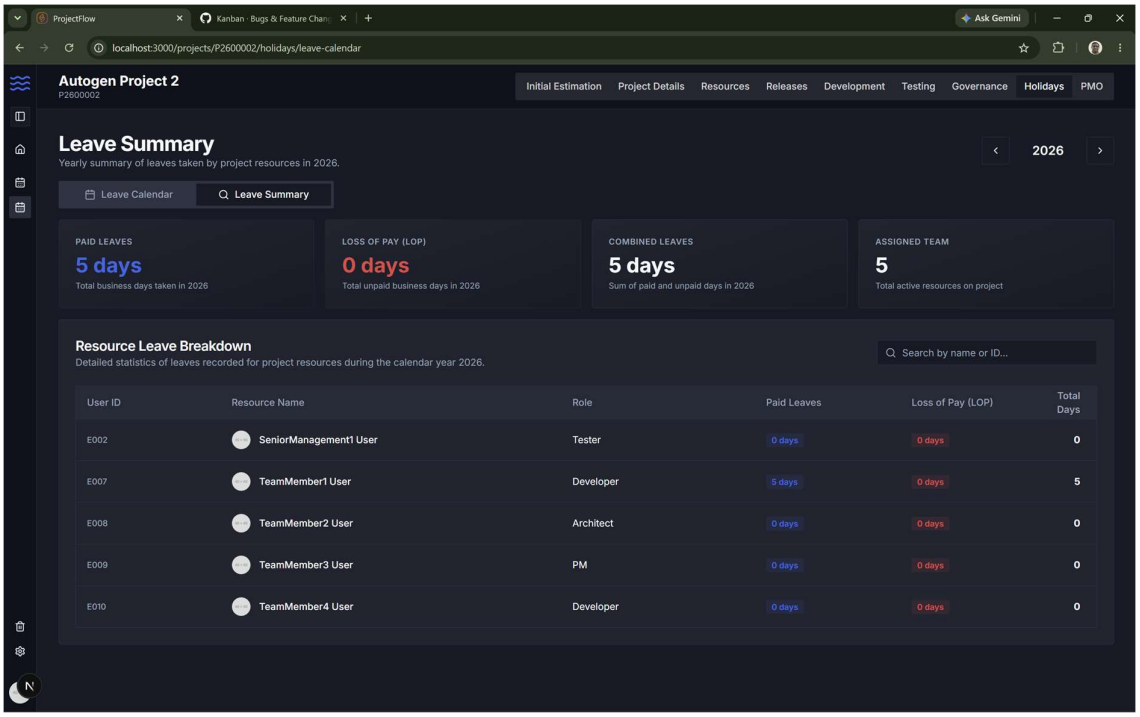


PMO

Project Documents

ProjectFlow as such do not provide storage facility. This is for the user to give the url to the destination of the project files which are either stored internally within the company or on cloud. This is to be used by the PMO/Audit team to verify.


General practice is that for a Vendor company, the SOW should be there to start the work. For product company, the requirements should be in place.

For permission to put the finished code in production, the sign off from the QA team is mandatory.

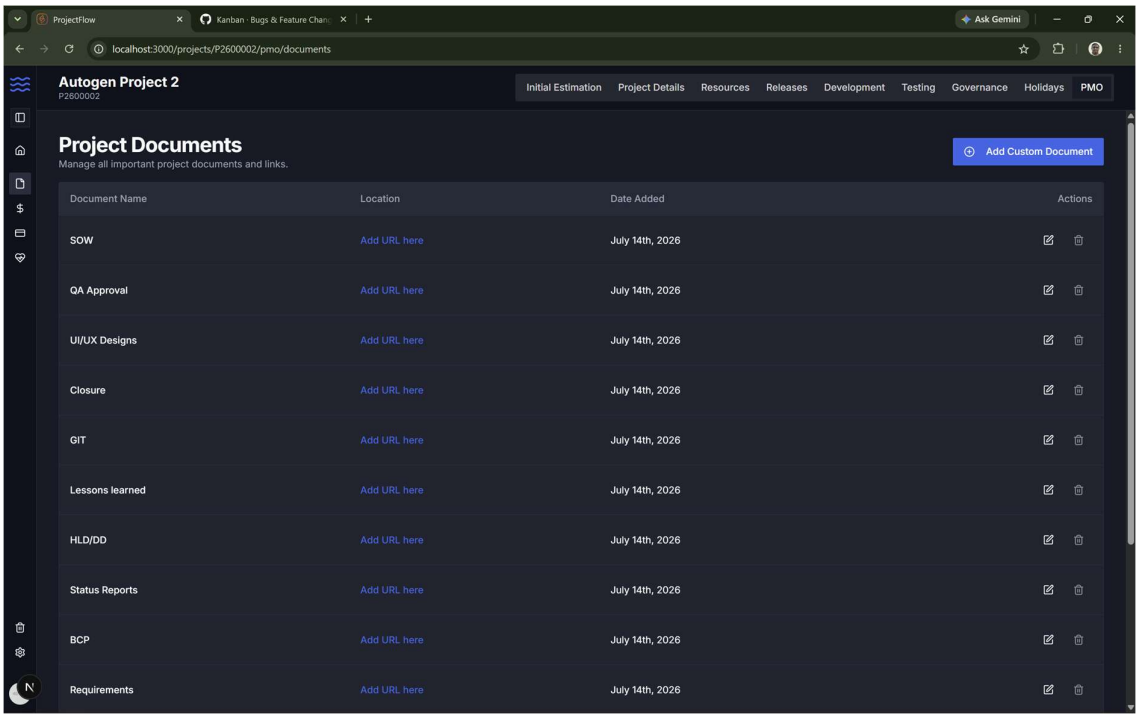

FB Billing (Fixed Bid Billing)


The Billed rate for the resource is taken from the resource page and cost rate is taken from the global user list.

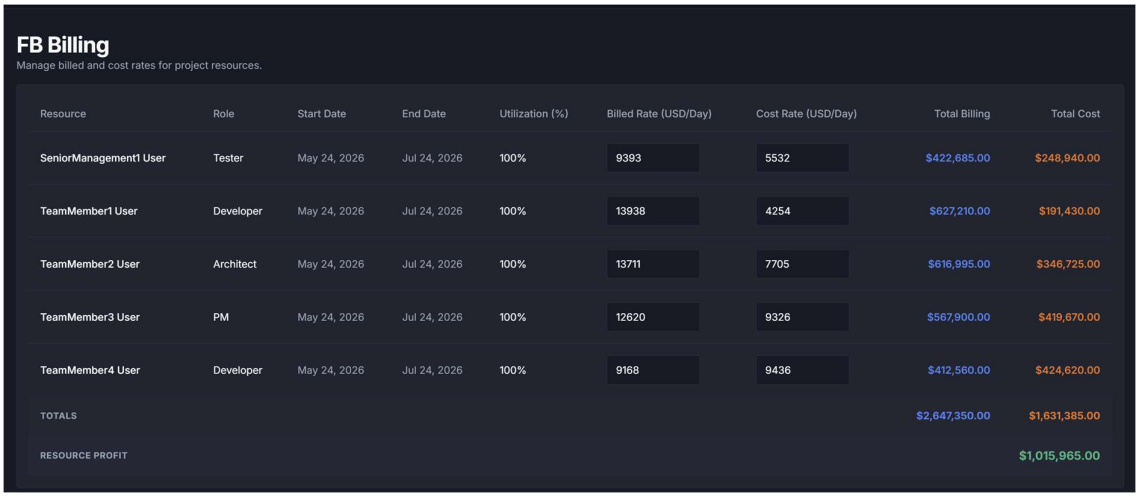

FB Billing

Manage billed and cost rates for project resources.

Resource	Role	Start Date	End Date	Utilization (%)	Billed Rate (USD/Day)	Cost Rate (USD/Day)	Total Billing	Total Cost
SeniorManagement1 User	Tester	May 24, 2026	Jul 24, 2026	100%	9393	5532	$422,685.00	$248,940.00
TeamMember1 User	Developer	May 24, 2026	Jul 24, 2026	100%	13938	4254	$627,210.00	$191,430.00
TeamMember2 User	Architect	May 24, 2026	Jul 24, 2026	100%	13711	7705	$616,995.00	$346,725.00
TeamMember3 User	PM	May 24, 2026	Jul 24, 2026	100%	12620	9326	$567,900.00	$419,670.00
TeamMember4 User	Developer	May 24, 2026	Jul 24, 2026	100%	9168	9436	$412,560.00	$424,620.00
TOTALS							$2,647,350.00	$1,631,385.00
RESOURCE PROFIT								$1,015,965.00

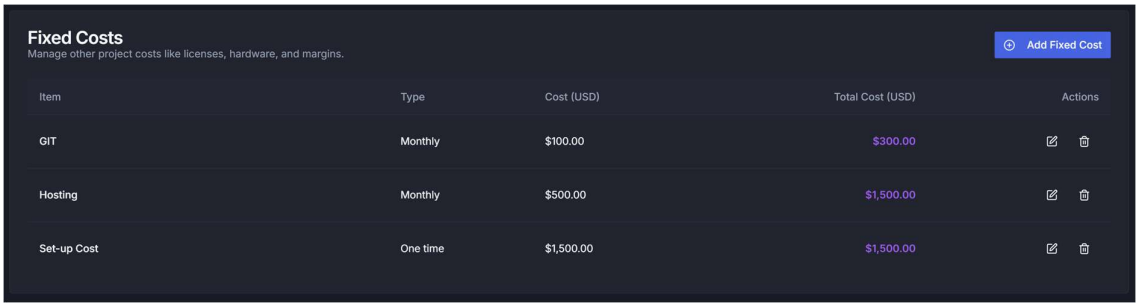


Fixed Costs

Manage other project costs like licenses, hardware, and margins.

Add Fixed Cost

Item	Type	Cost (USD)	Total Cost (USD)	Actions
GIT	Monthly	$100.00	$300.00	
Hosting	Monthly	$500.00	$1,500.00	
Set-up Cost	One time	$1,500.00	$1,500.00	

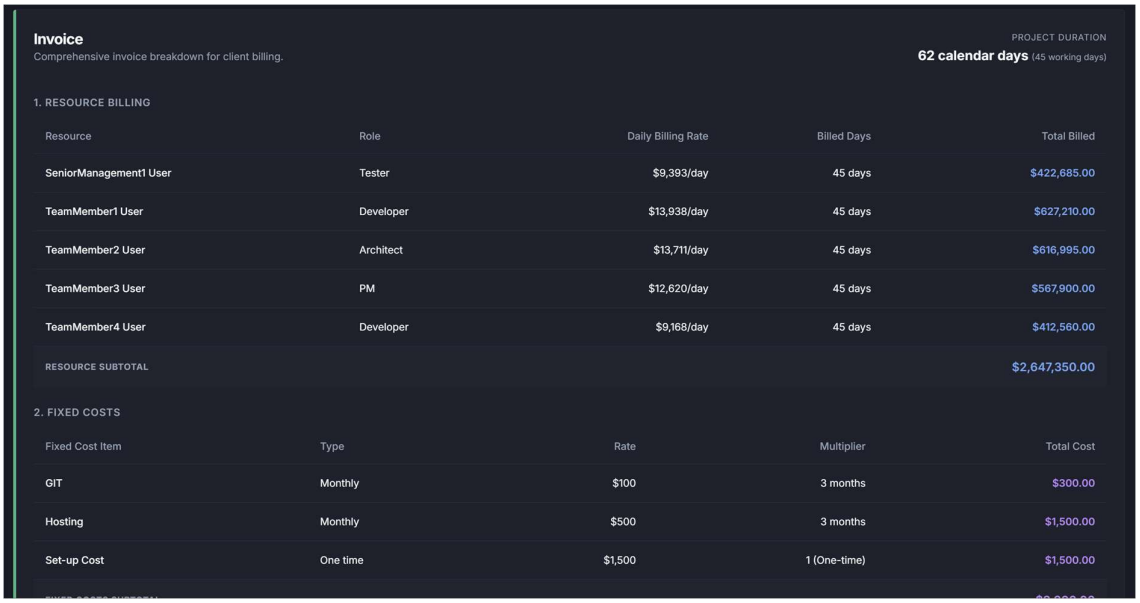

Invoice

Comprehensive invoice breakdown for client billing.

PROJECT DURATION

62 calendar days (45 working days)

1. RESOURCE BILLING


Resource	Role	Daily Billing Rate	Billed Days	Total Billed
SeniorManagement1 User	Tester	$9,393/day	45 days	$422,685.00
TeamMember1 User	Developer	$13,938/day	45 days	$627,210.00
TeamMember2 User	Architect	$13,711/day	45 days	$616,995.00
TeamMember3 User	PM	$12,620/day	45 days	$567,900.00
TeamMember4 User	Developer	$9,168/day	45 days	$412,560.00
RESOURCE SUBTOTAL				$2,647,350.00


2. FIXED COSTS

Fixed Cost Item	Type	Rate	Multiplier	Total Cost
GIT	Monthly	$100	3 months	$300.00
Hosting	Monthly	$500	3 months	$1,500.00
Set-up Cost	One time	$1,500	1 (One-time)	$1,500.00

FB Payment Milestones

Milestones are created when the client is releasing payment based on certain milestone completions for delivery. The status of the milestones are tracked with history.

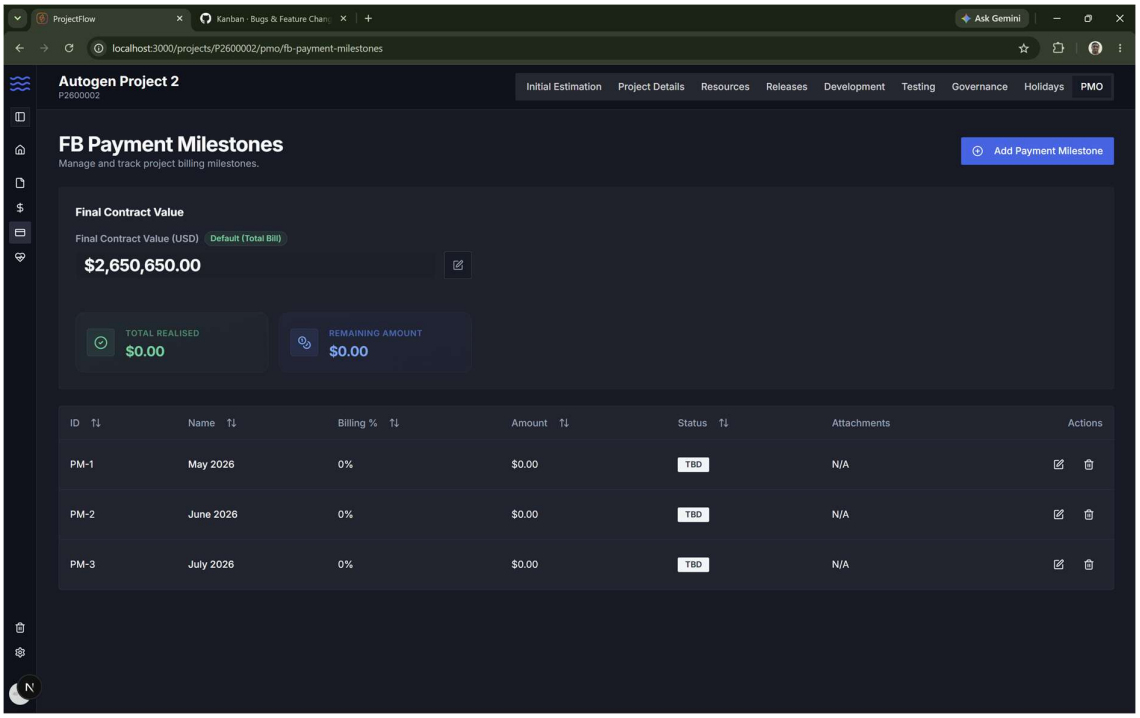


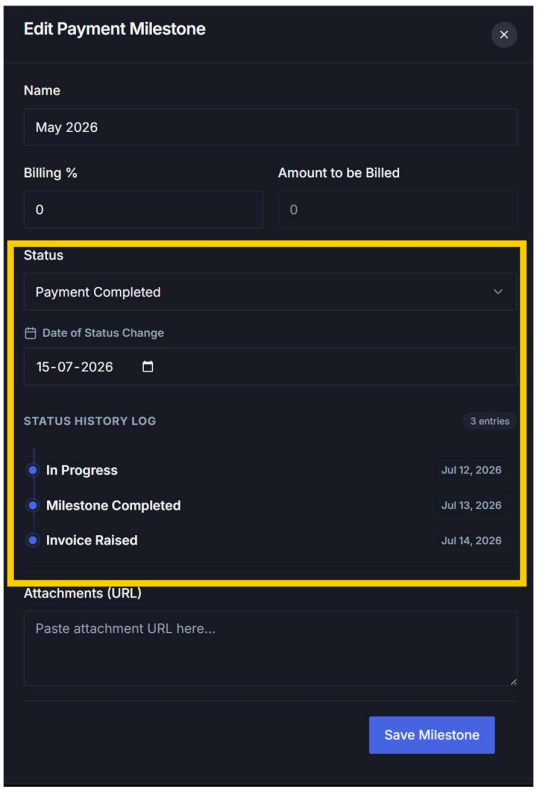

Business Continuity


The first two sections stores the environment details and their expiration dates and the code repositories and expiration dates so that even if there is a change in PM/resources over time, they would not have to run for these details at the last minute.


When a resource is added to the project, if they are marked for business continuity, then their names will be seen under BCP resources

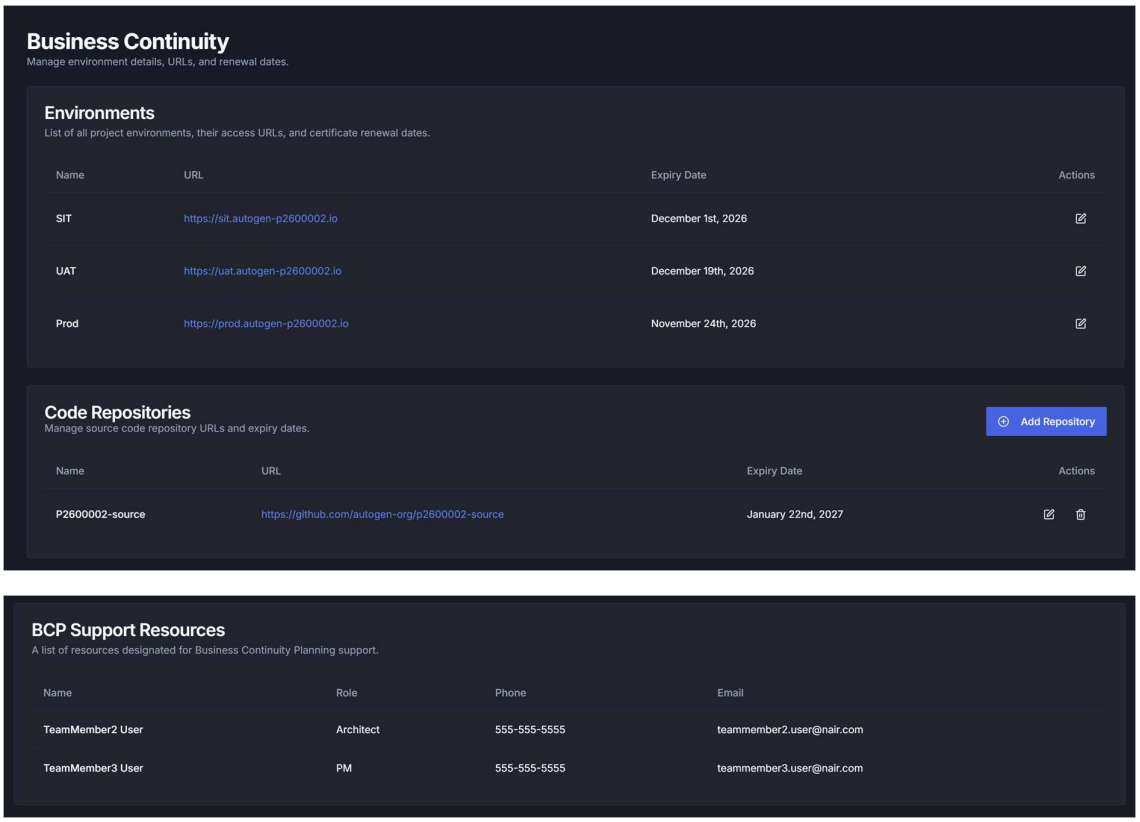



TnM Billing (Time & Matierial)

Similar to FB billing, but instead of one full bill, billing is done monthly.



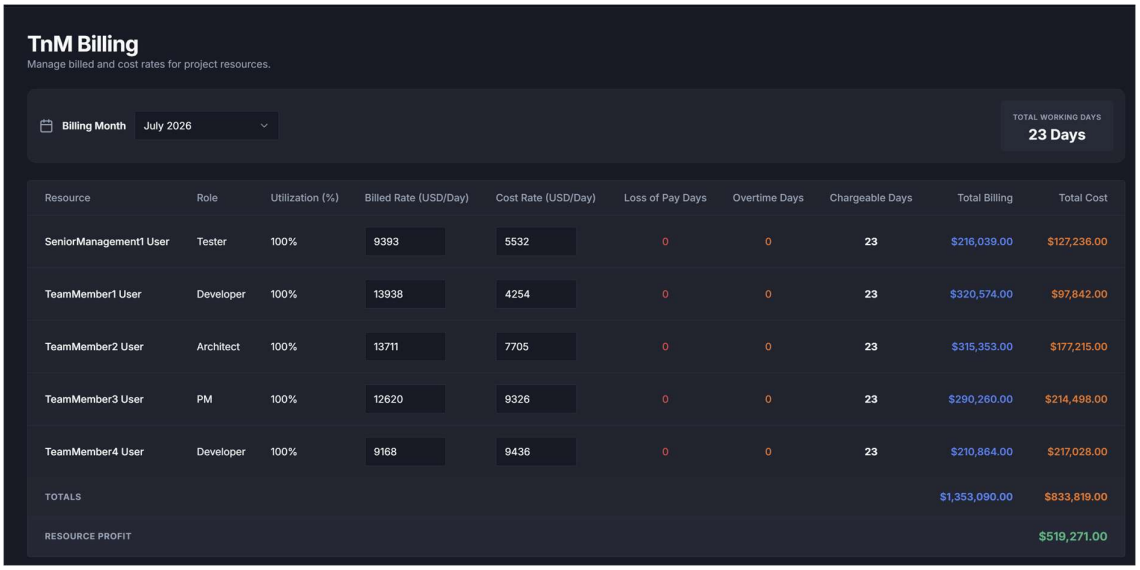

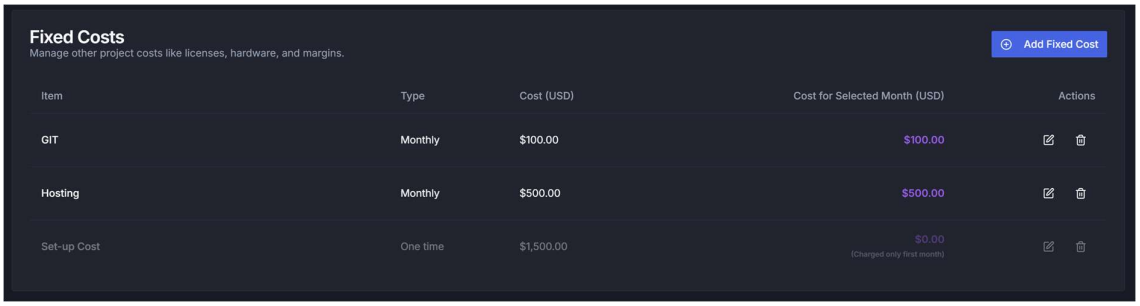

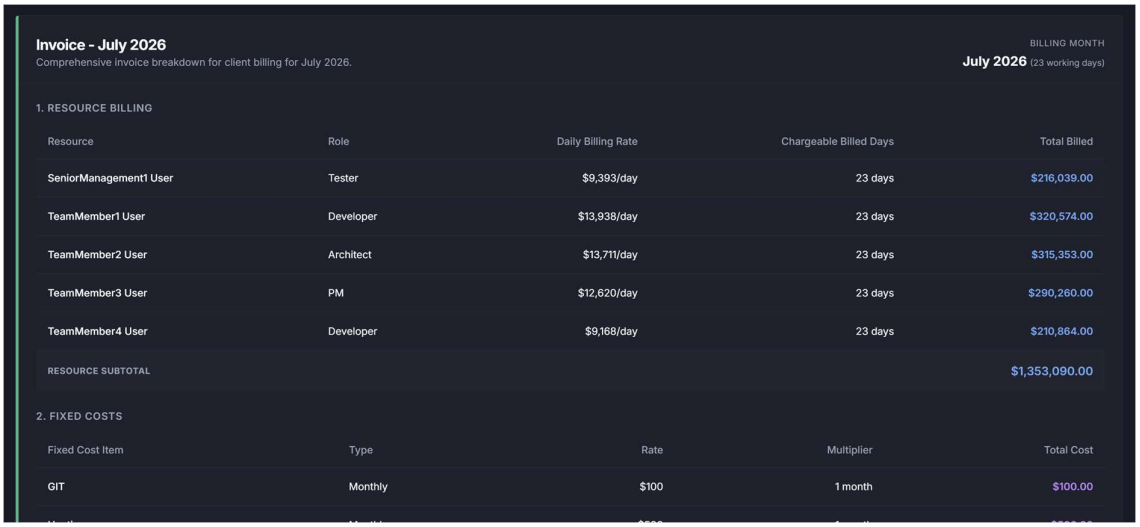

Invoice - July 2026
Comprehensive invoice breakdown for client billing for July 2026.

BILLING MONTH
July 2026 (23 working days)

1. RESOURCE BILLING


Resource	Role	Daily Billing Rate	Chargeable Billed Days	Total Billed
SeniorManagement1 User	Tester	$9,393/day	23 days	$216,039.00
TeamMember1 User	Developer	$13,938/day	23 days	$320,574.00
TeamMember2 User	Architect	$13,711/day	23 days	$315,353.00
TeamMember3 User	PM	$12,620/day	23 days	$290,260.00
TeamMember4 User	Developer	$9,168/day	23 days	$210,864.00
RESOURCE SUBTOTAL				$1,353,090.00

2. FIXED COSTS

Fixed Cost Item	Type	Rate	Multiplier	Total Cost
GIT	Monthly	$100	1 month	$100.00

TnM Payment Milestones

Similar to FB milestones, but instead of milestones, it will be months.

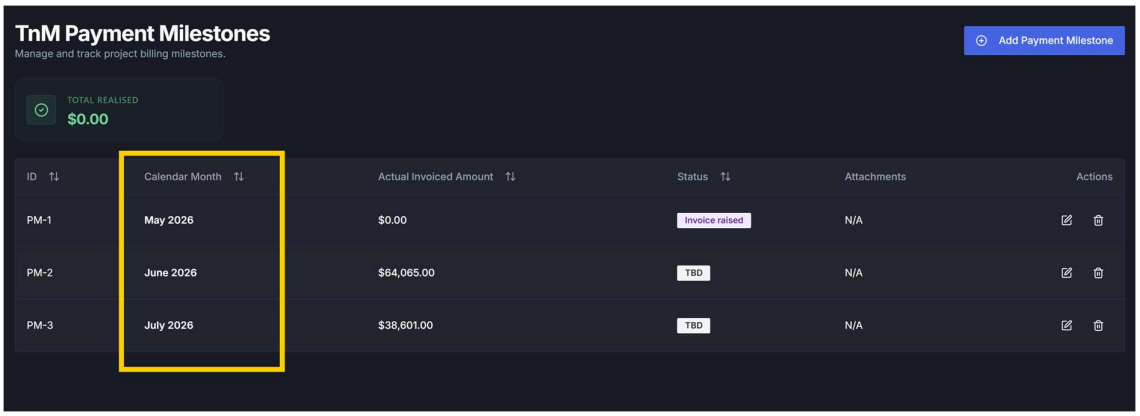

TnM Payment Milestones
Manage and track project billing milestones.

Add Payment Milestone

TOTAL REALISED
$0.00

ID	Calendar Month	Actual Invoiced Amount	Status	Attachments	Actions
PM-1	May 2026	$0.00	Invoice raised	N/A	
PM-2	June 2026	$64,065.00	TBD	N/A	
PM-3	July 2026	$38,601.00	TBD	N/A	


6. Admin Flow

Portfolio Settings

Access Settings


Page Access

Here the Admin can select which pages each role can view.

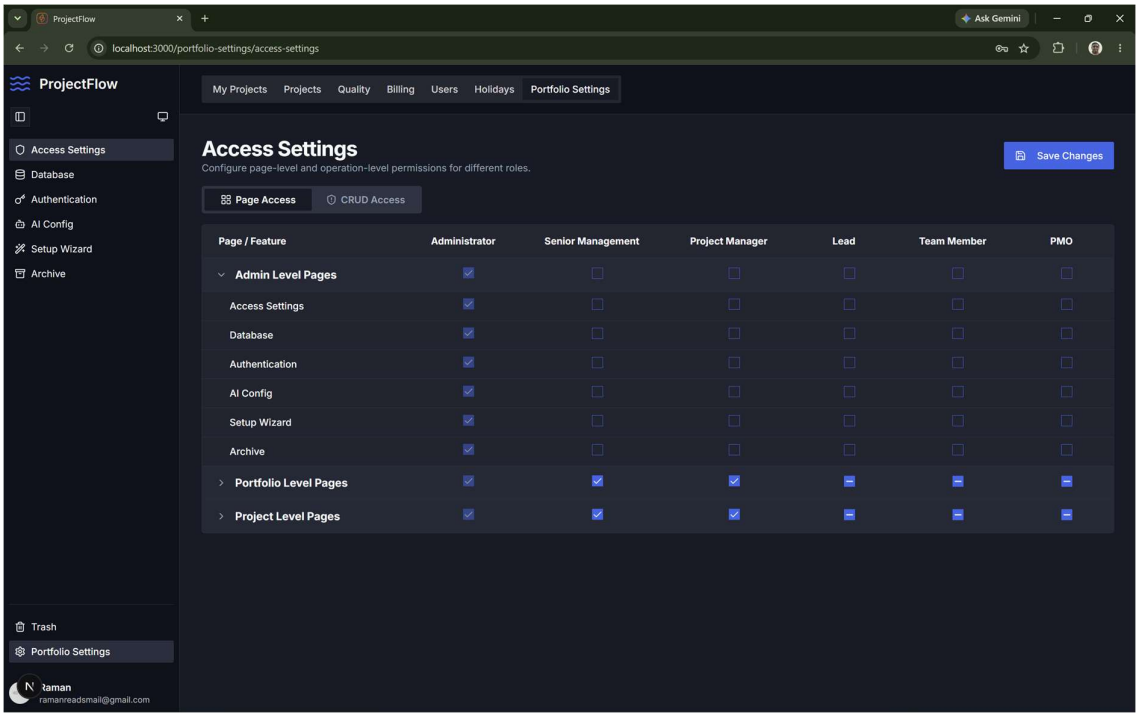


CRUD Access

Here the Admin can select the CRUD access levels for each role.

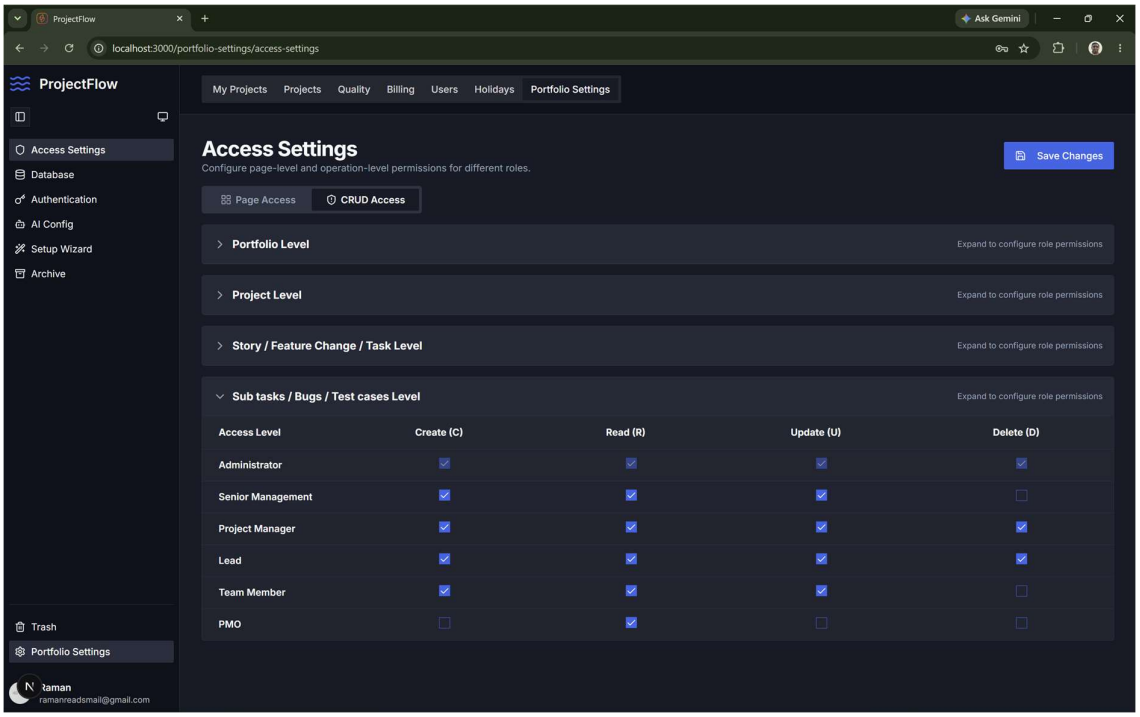


Database

For Admin to change settings in case of changes.

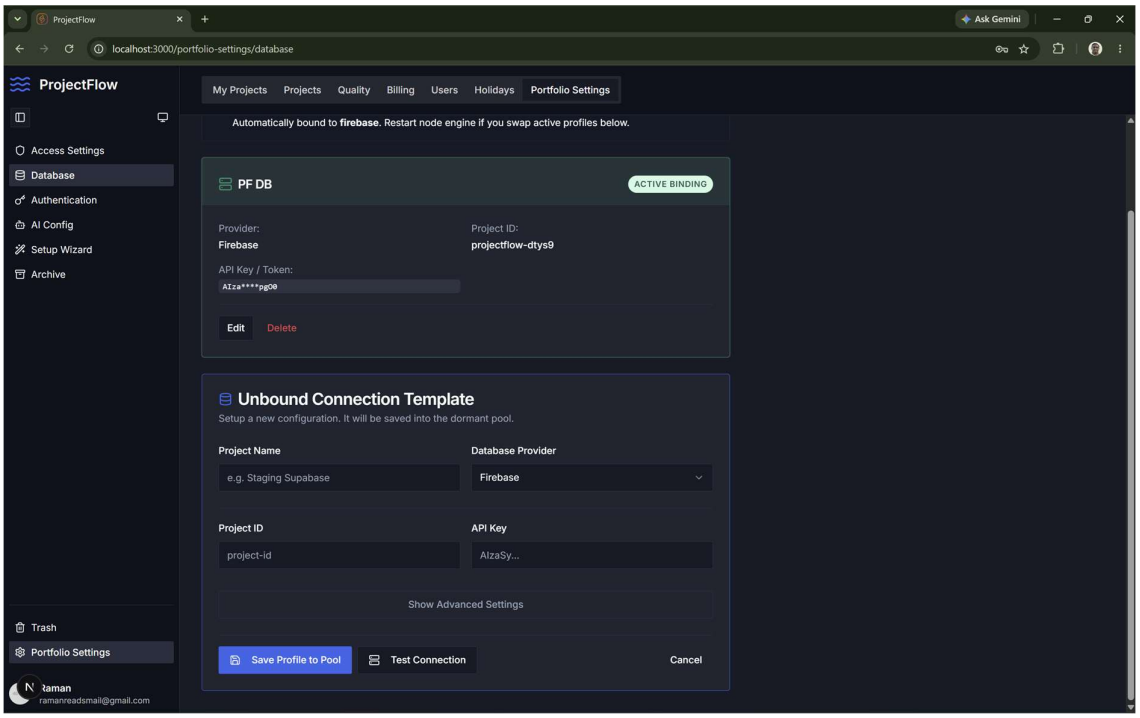


Authentication


For Admin to change settings in case of changes.

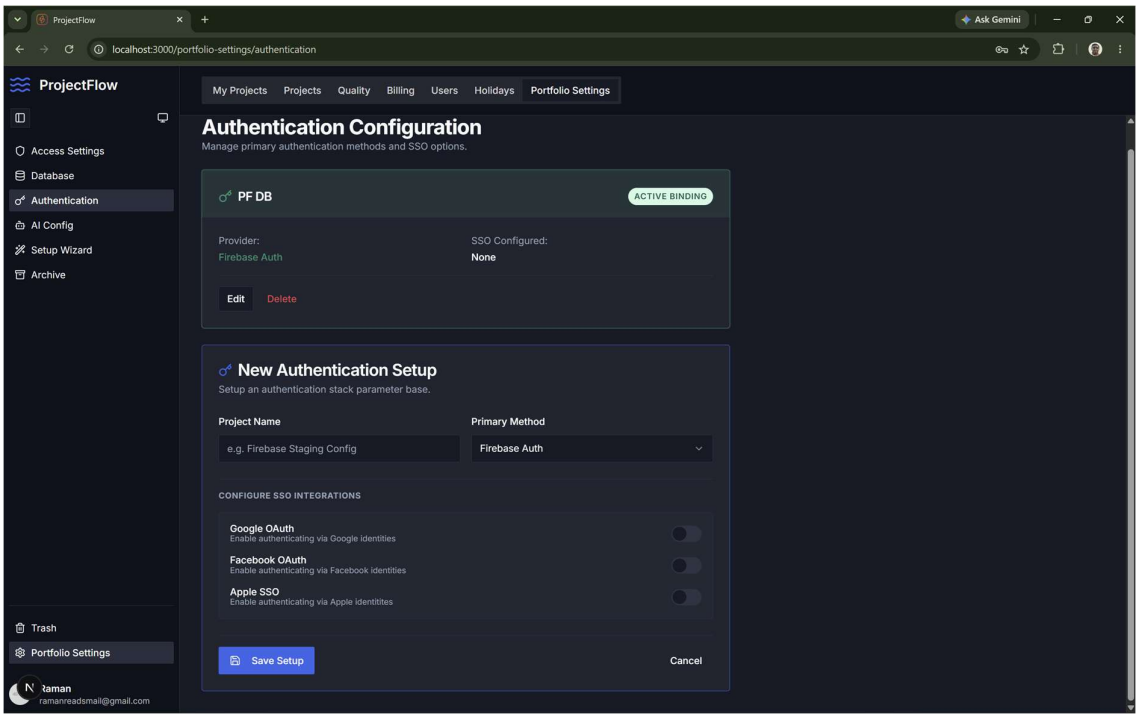

AI Configuration


For Admin to change settings in case of changes.

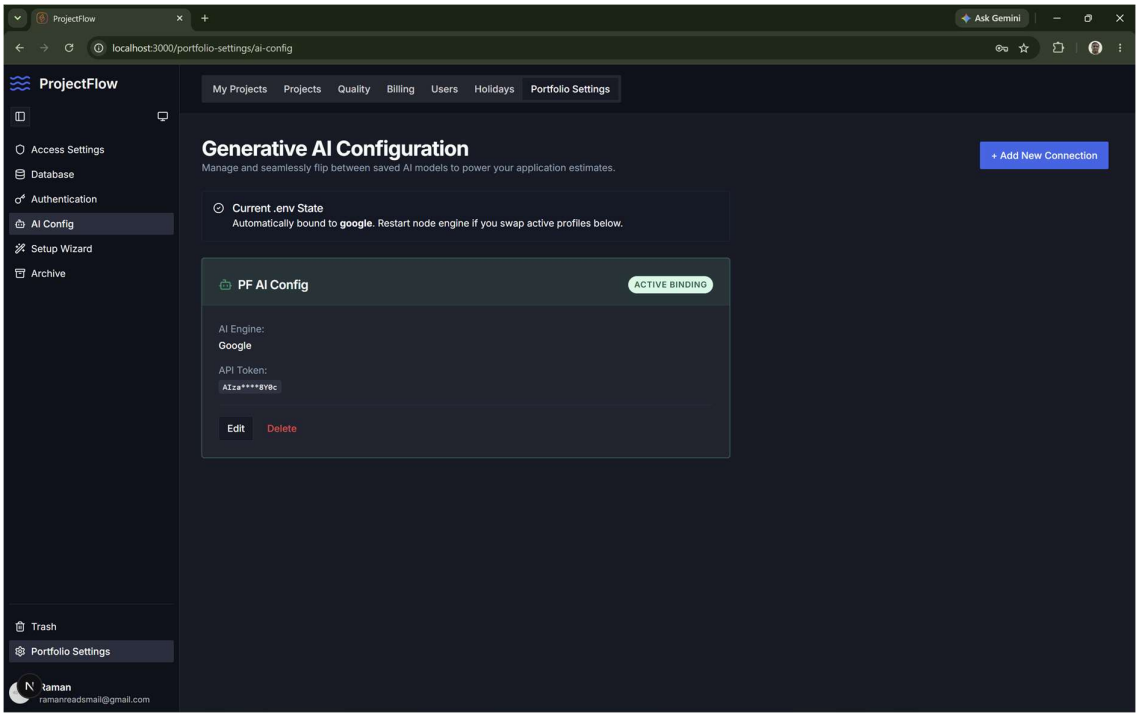

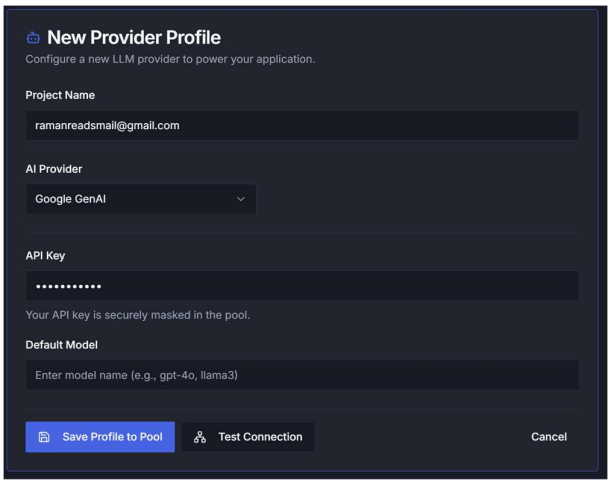

Archive

For Admin to enable and change archive settings.

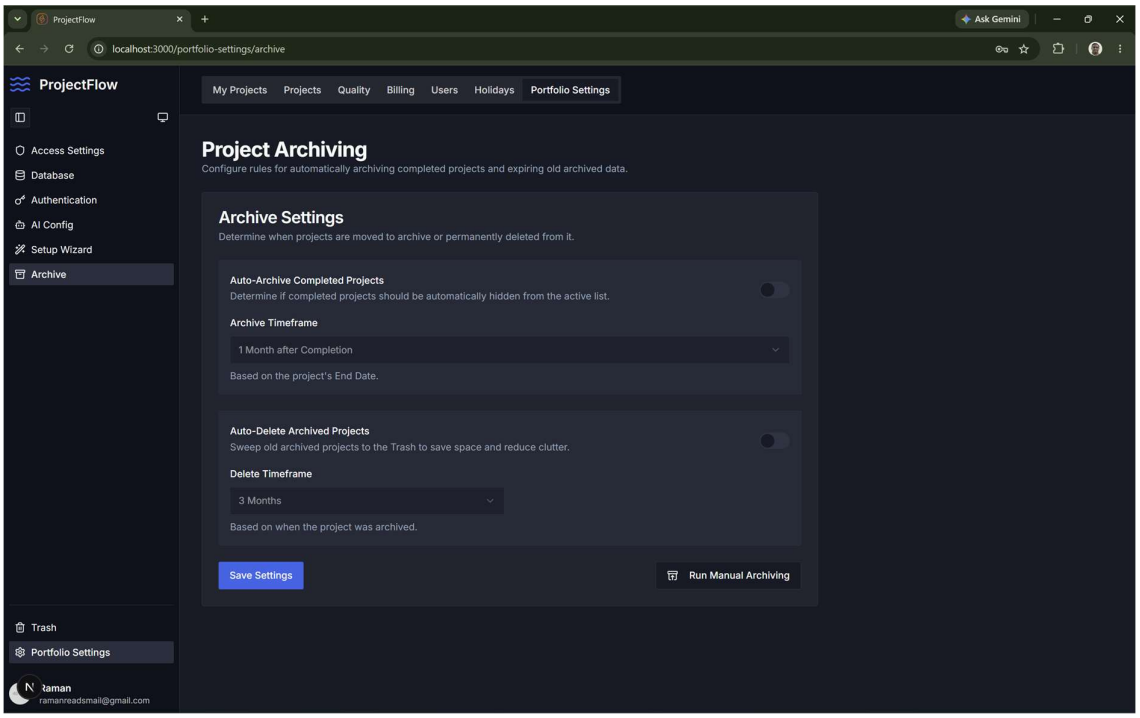

Trash

Before 30 days of final deletion of Portfolio items, Admin can restore from here.

